

Progress at WIPP

Presented to Idaho Citizens Advisory Board




Brad Bugger
Idaho Cleanup Project

February 17, 2016


Significant WIPP Accomplishments - 2015

- Ground Control – *catch up bolting 90% complete*
- Radiological risk reduction – *applications of water spray allowed down-posting of airborne contamination areas in all but panel 7*
- Electrical restoration - *completed*

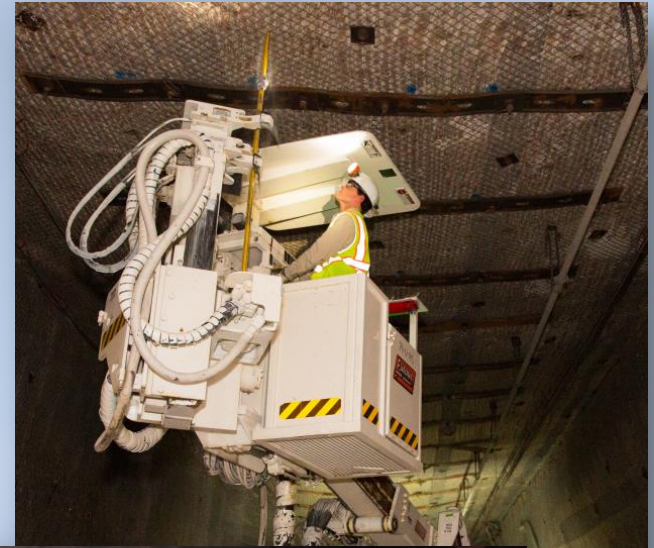

Significant WIPP Accomplishments - 2015

- Restoration of underground safety systems – *completed*
- Revitalization of Safety Management Programs
- AIB corrective actions – *prestart items near completion*
- Installation of the Interim ventilation system (in progress)

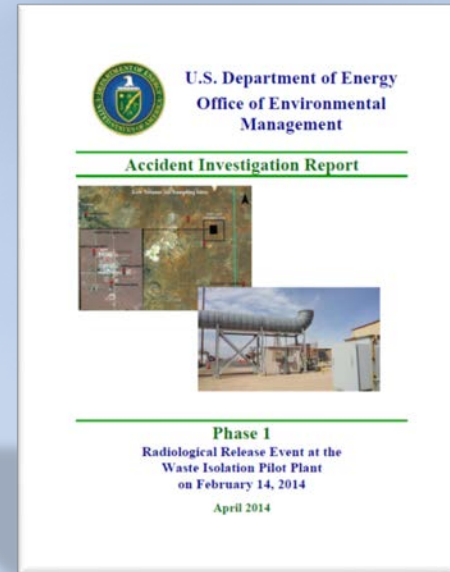


Recent WIPP Activities

- CD-1 for a new permanent ventilation system was approved by DOE Headquarters in December 2015 - the alternative chosen was:
 - Safety Significant Ventilation System
 - New Exhaust Shaft
- New integrated performance measurement baseline (IPMB) integrating recovery with base activities at the site, including capital asset projects –
 - Approved on January 19th
 - Sets target date for restart in December of 2016
 - Stakeholder workshop scheduled for February 19th

WIPP IPMB – BASELINE SCHEDULE

- Key Activity / Milestone Dates

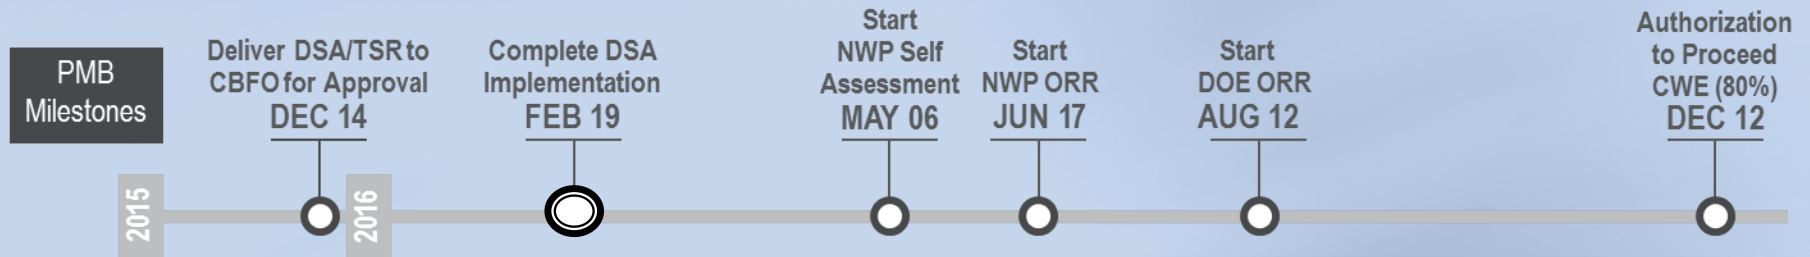

Path Forward for 2016

Key Restart Activities:

- DSA 3009-2014 Approval and Implementation
- Temporary Ventilation Operational
- Integrated Cold Operations
- Contractor Operational Readiness Review
- DOE Operational Readiness Review

