



Cheniere Energy, Inc.  
700 Milam Street, Suite 1900  
Houston, Texas 77002  
phone: 713.375.5000  
fax: 713.375.6000

Rec'd DOE/FE via FERGAS 3/29/2019

March 29, 2019

U.S. Department of Energy  
Office of Fossil Energy Natural Gas Regulatory Activities  
Attention: Larine Moore, Docket Room Manager Docket Room FE-34  
P.O. Box 44375  
Washington, DC 20026-4375

Re: Cheniere Marketing, LLC and Corpus Christi Liquefaction, LLC  
DOE Semi-Annual Report for Period for September 1, 2018, through February 28, 2019  
FE Docket Nos. 12-97-LNG & 12-99-LNG  
DOE/FE Order Nos. 3638, 3164 and 3164-A

Dear Ms. Moore:

Pursuant to the above-referenced Orders, Cheniere Marketing, LLC and Corpus Christi Liquefaction, LLC (collectively, "Cheniere") herein submits its semi-annual report for the period September 1, 2018, through February 28, 2019, describing the progress of the Corpus Christi Liquefaction Project ("Project"). This report covers the construction activities for the Project authorized under FERC Docket No. CP12-507-000. Please refer to Attachment A for the Monthly Reports for construction activities which were submitted to Federal Energy Regulatory Commission under FERC Docket No. CP12-507-000 during the reporting period.

Additionally, Cheniere is providing information relating to the status of long term contracts that have been executed during the reporting period. On September 17, 2018, Cheniere Marketing, LLC ("Cheniere Marketing") entered into a liquefied natural gas ("LNG") sale and purchase agreement ("SPA") with Vitol Inc. ("Vitol"). Under the SPA, Vitol has agreed to purchase approximately 0.7 million tonnes per annum of LNG from Cheniere Marketing on a free on board basis for a term of approximately 15 years beginning in 2018. The purchase price for LNG is indexed to the monthly Henry Hub price, plus a fee.

Please call Taylor Johnson or me at 713-375-5000 if you have any questions.

Sincerely,

Karri Mahmoud  
Cheniere Marketing, LLC and Corpus Christi Liquefaction, LLC

Cheniere Marketing, LLC and Corpus Christi Liquefaction, LLC

DOE Semi-Annual Report for Period September 1, 2018, through February 28, 2019

## **ATTACHMENT A**

**CORPUS CHRISTI LIQUEFACTION PROJECT**

**Corpus Christi, Texas**

**MONTHLY PROGRESS REPORT  
SEPTEMBER 2018  
FERC DOCKET NO. CP12-507-000**

Corpus Christi Liquefaction, LLC  
September 2018 Monthly Progress Report

**Table of Contents**

1.0	Executive Summary .....	3
2.0	Project Highlights .....	3
3.0	Environmental, Safety, and Health Progress .....	3
4.0	Schedule .....	3
5.0	Construction .....	4
6.0	Permitting and Environmental .....	6
7.0	Progress Pictures .....	7

## 1.0 Executive Summary

This report covers activities for the CCL Stage 1 (Trains 1 and 2, Tanks A and C, OSBL, West Jetty and East Jetty Civil Works) and CCL Stage 2 (Train 3, Tank B and East Jetty Topsides) projects that occurred during the month of September 2018.

Stage 1 Engineering and Procurement are now 100.0% complete. Subcontract and direct hire construction work are 83.6% and 86.9% complete, respectively. Overall project completion for Stage 1 is 93.9%. Train 1 is projected to achieve substantial completion in the 1<sup>st</sup> half of 2019 and Train 2 in the 2<sup>nd</sup> half of 2019.

Stage 2 Engineering is 79.2% complete. Procurement is 57.3% complete. Subcontract and direct hire construction work are 5.8% and 5.9% complete, respectively. Overall project completion for Stage 2 is 36.3%.

## 2.0 Project Highlights

Stage 1 continued progressing work in pipe restoration and insulation of critical path systems. Major accomplishments in September included: placing the dry flare in service, turnover of Train 1 Ethylene compressors and running of the ethylene compressors on nitrogen. Startup continued with leak checks and cause and effects of various systems. Construction has turned 261 systems over to Startup through the end of September.

Stage 2 continued site excavation, concrete, structural steel erection, underground piping, and aboveground piping activities. The team continued shoring, decking, rebar, and formwork in the compressor area.

## 3.0 Environmental, Safety, and Health Progress – Stage 1

	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>
Bechtel	18	700	32	1248	8	59	0	1
Subcontractor	0	0	0	0	0	0	0	2
Total	18	700	32	1248	8	59	0	3

1. ITD = Inception to Date.

### Environmental, Safety, and Health Progress – Stage 2

	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>
Bechtel	0	11	2	15	0	0	0	0
Subcontractor	0	0	0	0	0	0	0	0
Total	0	11	2	15	0	0	0	0

1. ITD = Inception to Date.

## 4.0 Schedule

Train 1 is projected to achieve substantial completion in the 1<sup>st</sup> half of 2019 and Train 2 in the 2<sup>nd</sup> half of 2019. Activities planned for the month of October 2018 are on track.

Corpus Christi Liquefaction, LLC  
September 2018 Monthly Progress Report

**5.0 Construction**

Area	Construction Activities in September	Planned Work for October
<b>(Stage 1 Project)</b>  ISBL Train 1 Compressor Area / Cryogenic Piperack / Propane Refrigeration	<ul style="list-style-type: none"> <li>• Continued cable pulling and terminations in all areas to support loop checks.</li> <li>• Continued pipe insulation.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue pipe insulation.</li> <li>• Continue cable pulling and terminations.</li> <li>• Continue work on process systems to support the turnover skyline.</li> </ul>
Train 2	<ul style="list-style-type: none"> <li>• Continued initial lube oil flushes.</li> <li>• Continued erection of structural steel.</li> <li>• Continued installation of aboveground pipe.</li> <li>• Continued cable pulling and terminations to prepare for upcoming energization.</li> <li>• Completed installation of gas generators.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue installation of above ground pipe and testing.</li> <li>• Continue initial mineral lube oil flushes.</li> <li>• Continue cable pulling and terminations to prepare for upcoming energization.</li> </ul>
OSBL / Refrigerant Storage Area / Process Piperack	<ul style="list-style-type: none"> <li>• Continued concrete and steel activities.</li> <li>• Continued mechanical equipment activities.</li> <li>• Continued installation, testing, drying/blowing, and restoration of aboveground pipe.</li> <li>• Continued cable tray and conduit installation.</li> <li>• Continued cable pulling.</li> <li>• Continued loop checks.</li> <li>• Continued installation of lights and fixtures/devices.</li> <li>• Continued pipe insulation.</li> <li>• Continued installation of vapor barrier fence and light pole installation.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue piping program.</li> <li>• Continue installation of cable tray.</li> <li>• Continue conduit installation.</li> <li>• Continue cable pulling.</li> <li>• Continue loop checks.</li> <li>• Continue pipe insulation installation.</li> <li>• Continue with civil works.</li> </ul>
LNG Tank A	<ul style="list-style-type: none"> <li>• Completed nitrogen purge.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue nitrogen purge.</li> <li>• Continue logo installation.</li> </ul>
LNG Tank C	<ul style="list-style-type: none"> <li>• Completed suspended deck insulation and began closure of tank in preparation for nitrogen purge.</li> </ul>	<ul style="list-style-type: none"> <li>• Commence nitrogen purge.</li> <li>• Continue logo installation.</li> </ul>
Access Roads / Buildings	<ul style="list-style-type: none"> <li>• N/A</li> </ul>	<ul style="list-style-type: none"> <li>• N/A</li> </ul>

Corpus Christi Liquefaction, LLC  
September 2018 Monthly Progress Report

Area	Construction Activities in September	Planned Work for October
Marine Area	<ul style="list-style-type: none"> <li>• N/A</li> </ul>	<ul style="list-style-type: none"> <li>• N/A</li> </ul>
<b>(Stage 2 Project)</b>  ISBL and OSBL Train 3	<ul style="list-style-type: none"> <li>• Continued sitework, concrete and underground pipe activities.</li> <li>• Continued shoring and decking in Compressor area.</li> <li>• Continued installation of underground amine piping.</li> <li>• Continued installation of cryo rack and acid gas removal steel.</li> <li>• Continued double jointing of aboveground pipe.</li> <li>• Continued pipe loading.</li> <li>• Continued welding of HDPE pipe.</li> <li>• Commenced rebar and formwork.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue sitework preparation activities.</li> <li>• Continue mudmat placement.</li> <li>• Continue rebar and formwork activities.</li> <li>• Continue structural concrete placement.</li> <li>• Continue installation of grounding grid.</li> <li>• Continue structural steel installation.</li> <li>• Continue double jointing of aboveground pipe.</li> <li>• Continue amine metallic piping.</li> <li>• Continue loading aboveground piping.</li> <li>• Complete shoring and decking installation.</li> </ul>
Tank B	<ul style="list-style-type: none"> <li>• Continued outer wall liner.</li> <li>• Continued rebar and formwork.</li> <li>• Commenced roof panel assembly.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue rebar and formwork activities.</li> <li>• Continue outer wall liner work.</li> <li>• Continue roof panel assembly.</li> </ul>
Marine Area East Jetty Topside	<ul style="list-style-type: none"> <li>• N/A</li> </ul>	<ul style="list-style-type: none"> <li>• N/A</li> </ul>

## 6.0 Permitting and Environmental

No updates to any environmental permits or the Emergency Response Plan for project construction were made during the September reporting period.

### Summary of Problems, Non-Compliances, and Corrective Actions

Date	Description
N/A	

### Agency Contacts/Inspections

Agency	Name	Date	Location/Activity
N/A			

## 7.0 Progress Pictures



*Train 1 Area Paving*



*West Jetty Construction Progress*

Corpus Christi Liquefaction, LLC  
September 2018 Monthly Progress Report



*Preparation for Tank A Logo Painting*



*Ground Flare Construction Progress*

Corpus Christi Liquefaction, LLC  
September 2018 Monthly Progress Report



*LNG Tank B Overview*



*Tank B Outer Wall Hanging*

Corpus Christi Liquefaction, LLC  
September 2018 Monthly Progress Report



*Train 3 Rebar Decking Compressor Deck*



*Site-wide view*

**CORPUS CHRISTI LIQUEFACTION PROJECT**

**Corpus Christi, Texas**

**MONTHLY PROGRESS REPORT  
OCTOBER 2018  
FERC DOCKET NO. CP12-507-000**

Corpus Christi Liquefaction, LLC  
October 2018 Monthly Progress Report

**Table of Contents**

1.0	Executive Summary .....	3
2.0	Project Highlights .....	3
3.0	Environmental, Safety, and Health Progress .....	3
4.0	Schedule .....	3
5.0	Construction .....	4
6.0	Permitting and Environmental .....	6
7.0	Progress Pictures .....	7

## 1.0 Executive Summary

This report covers activities for the CCL Stage 1 (Trains 1 and 2, Tanks A and C, OSBL, West Jetty and East Jetty Civil Works) and CCL Stage 2 (Train 3, Tank B and East Jetty Topsides) projects that occurred during the month of October 2018.

Stage 1 Engineering and Procurement are now 100.0% complete. Subcontract and direct hire construction work are 84.2% and 89.3% complete, respectively. Overall project completion for Stage 1 is 94.9%. Train 1 is projected to achieve substantial completion in the 1<sup>st</sup> half of 2019 and Train 2 in the 2<sup>nd</sup> half of 2019.

Stage 2 Engineering is 82.2% complete. Procurement is 58.3% complete. Subcontract and direct hire construction work are 6.8% and 7.4% complete, respectively. Overall project completion for Stage 2 is 37.7%.

## 2.0 Project Highlights

Stage 1 continued progressing work in pipe restoration and insulation of critical path systems. Major accomplishments in October included: placing Train 1 entirely in CSU control. The team is now focused on preparing for defrost and cooldown. Construction has turned 284 systems over to Startup through the end of October.

Stage 2 continued with concrete foundation and underground piping installation. Steel erection continues to progress, and rebar are well under way with the first compressor deck placement completed in October. LNG Tank B concrete wall pours and roof panel assembly are in progress.

## 3.0 Environmental, Safety, and Health Progress – Stage 1

	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>
Bechtel	14	714	32	1280	5	64	0	1
Subcontractor	0	0	0	0	0	0	0	2
Total	14	714	32	1280	5	64	0	3

1. ITD = Inception to Date.

### Environmental, Safety, and Health Progress – Stage 2

	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>
Bechtel	1	12	2	17	1	1	0	0
Subcontractor	0	0	0	0	0	0	0	0
Total	1	12	2	17	1	1	0	0

1. ITD = Inception to Date.

## 4.0 Schedule

Train 1 is projected to achieve substantial completion in the 1<sup>st</sup> half of 2019 and Train 2 in the 2<sup>nd</sup> half of 2019. Activities planned for the month of November 2018 are on track.

Corpus Christi Liquefaction, LLC  
October 2018 Monthly Progress Report

## 5.0 Construction

Area	Construction Activities in October	Planned Work for November
<b>(Stage 1 Project)</b>  ISBL Train 1 Compressor Area / Cryogenic Piperack / Propane Refrigeration	<ul style="list-style-type: none"> <li>• Continued cable pulling and terminations in all areas to support loop checks.</li> <li>• Continued pipe insulation.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue pipe insulation.</li> <li>• Continue cable pulling and terminations.</li> <li>• Continue work on process systems to support the turnover skyline.</li> </ul>
Train 2	<ul style="list-style-type: none"> <li>• Continued initial lube oil flushes.</li> <li>• Continued erection of structural steel.</li> <li>• Continued installation of aboveground pipe.</li> <li>• Continued cable pulling and terminations to prepare for upcoming energization.</li> <li>• Commenced installation of dry gas seals.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue installation of aboveground pipe and testing.</li> <li>• Continue initial mineral lube oil flushes.</li> <li>• Continue cable pulling and terminations to prepare for upcoming energization.</li> <li>• Complete installation of dry gas seals.</li> </ul>
OSBL / Refrigerant Storage Area / Process Piperack	<ul style="list-style-type: none"> <li>• Continued concrete and steel activities.</li> <li>• Continued mechanical equipment activities.</li> <li>• Continued cable tray and conduit installation.</li> <li>• Continued cable pulling.</li> <li>• Continued loop checks.</li> <li>• Continued installation of lights and fixtures/devices.</li> <li>• Continued pipe insulation.</li> <li>• Continued installation of vapor barrier fence and light pole installation.</li> <li>• Completed installation, testing, drying/blowing, and restoration of aboveground pipe.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue installation of cable tray.</li> <li>• Continue conduit installation.</li> <li>• Continue cable pulling.</li> <li>• Continue loop checks.</li> <li>• Continue pipe insulation installation.</li> <li>• Continue with civil works.</li> </ul>
LNG Tank A	<ul style="list-style-type: none"> <li>• Commenced logo painting.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue logo installation.</li> </ul>
LNG Tank C	<ul style="list-style-type: none"> <li>• Commenced nitrogen purge.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue logo installation.</li> <li>• Continue nitrogen purge.</li> </ul>
Access Roads / Buildings	<ul style="list-style-type: none"> <li>• N/A</li> </ul>	<ul style="list-style-type: none"> <li>• N/A</li> </ul>

Corpus Christi Liquefaction, LLC  
October 2018 Monthly Progress Report

Area	Construction Activities in October	Planned Work for November
Marine Area	<ul style="list-style-type: none"> <li>• N/A</li> </ul>	<ul style="list-style-type: none"> <li>• N/A</li> </ul>
<b>(Stage 2 Project)</b>  ISBL and OSBL Train 3	<ul style="list-style-type: none"> <li>• Continued sitework, concrete and underground pipe activities.</li> <li>• Continued rebar and formwork.</li> <li>• Continued concrete placement.</li> <li>• Continued structural steel installation.</li> <li>• Continued installation of underground amine piping.</li> <li>• Continued installation of cryo pipe rack and acid gas removal steel.</li> <li>• Continued double jointing of aboveground pipe.</li> <li>• Completed shoring and decking in Compressor area.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue sitework preparation activities.</li> <li>• Continue mudmat placement.</li> <li>• Continue rebar and formwork activities.</li> <li>• Continue structural concrete placement.</li> <li>• Continue installation of grounding grid.</li> <li>• Continue installation of underground piping.</li> <li>• Continue structural steel installation.</li> <li>• Continue double jointing of aboveground pipe.</li> <li>• Continue loading aboveground piping.</li> <li>• Complete amine metallic piping.</li> </ul>
Tank B	<ul style="list-style-type: none"> <li>• Continued outer wall liner.</li> <li>• Continued rebar and formwork.</li> <li>• Continued roof panel assembly.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue rebar and formwork activities.</li> <li>• Continue outer wall liner work.</li> <li>• Continue roof panel assembly.</li> </ul>
Marine Area East Jetty Topside	<ul style="list-style-type: none"> <li>• N/A</li> </ul>	<ul style="list-style-type: none"> <li>• N/A</li> </ul>

## 6.0 Permitting and Environmental

No updates to any environmental permits or the Emergency Response Plan for project construction were made during the October reporting period.

### Summary of Problems, Non-Compliances, and Corrective Actions

Date	Description
N/A	

### Agency Contacts/Inspections

Agency	Name	Date	Location/Activity
FERC	Steven Kusy Wimberly Hoogendoorn	October 10-11, 2018	Construction Inspection. No deficiencies noted.

**7.0 Progress Pictures**



*Stage 1 - Train 2 Hot Oil Storage Drum Progress*



*Stage 1 - Train 2 Mercury Removal Bed Progress*

Corpus Christi Liquefaction, LLC  
October 2018 Monthly Progress Report



*Stage 1 - OSBL West Jetty Construction Progress*



*Stage 2 - LNG Tank B Progress*

Corpus Christi Liquefaction, LLC  
October 2018 Monthly Progress Report



*Stage 2 - Train 3 Compressor Substation Foundation Progress*



*Stage 2 - Train 3 Propane Refrigeration Walls Formwork*



*Stage 2 – Train 3 Pipe Installation Commencement at AGRU E01 rack*



Site-Wide View

**CORPUS CHRISTI LIQUEFACTION PROJECT**

**Corpus Christi, Texas**

**MONTHLY PROGRESS REPORT  
NOVEMBER 2018  
FERC DOCKET NO. CP12-507-000**

Corpus Christi Liquefaction, LLC  
November 2018 Monthly Progress Report

**Table of Contents**

1.0	Executive Summary .....	3
2.0	Project Highlights .....	3
3.0	Environmental, Safety, and Health Progress .....	3
4.0	Schedule .....	3
5.0	Construction .....	4
6.0	Permitting and Environmental .....	6
7.0	Progress Pictures .....	7

## 1.0 Executive Summary

This report covers activities for the CCL Stage 1 (Trains 1 and 2, Tanks A and C, OSBL, West Jetty and East Jetty Civil Works) and CCL Stage 2 (Train 3, Tank B and East Jetty Topsides) projects that occurred during the month of November 2018.

Stage 1 Engineering and Procurement are now 100.0% complete. Subcontract and direct hire construction work are 85.8% and 91.5% complete, respectively. Overall project completion for Stage 1 is 95.9%. Train 1 is projected to achieve substantial completion in the 1<sup>st</sup> half of 2019 and Train 2 in the 2<sup>nd</sup> half of 2019.

Stage 2 Engineering is 85.0% complete. Procurement is 61.6% complete. Subcontract and direct hire construction work are 7.5% and 9.5% complete, respectively. Overall project completion for Stage 2 is 40.3%.

## 2.0 Project Highlights

Stage 1 construction remains focused on completion of insulation of critical path systems.. The team also continued to focus on pipe testing and restoration. Major accomplishments in November included: defrost, cooldown, and production of first LNG.. Construction has turned 295 systems over to Startup through the end of November.

Stage 2 construction continued with site excavation, concrete placement, structural steel erection, underground piping, and aboveground piping activities. The team also installed the ethylene section of the compressor deck. Loading of aboveground pipe in the cryogenic and AGRU racks are also underway.

## 3.0 Environmental, Safety, and Health Progress – Stage 1

	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>
Bechtel	10	724	28	1308	1	65	0	1
Subcontractor	0	0	0	0	0	0	0	2
Total	10	724	28	1308	1	65	0	3

1. ITD = Inception to Date.

## Environmental, Safety, and Health Progress – Stage 2

	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>
Bechtel	3	15	2	19	2	3	0	0
Subcontractor	0	0	0	0	0	0	0	0
Total	3	15	2	19	2	3	0	0

1. ITD = Inception to Date.

## 4.0 Schedule

Train 1 is projected to achieve substantial completion in the 1<sup>st</sup> half of 2019 and Train 2 in the 2<sup>nd</sup> half of 2019. Activities planned for the month of December 2018 are on track.

Corpus Christi Liquefaction, LLC  
November 2018 Monthly Progress Report

**5.0 Construction**

Area	Construction Activities in November	Planned Work for December
<b>(Stage 1 Project)</b>  ISBL Train 1 Compressor Area / Cryogenic Piperack / Propane Refrigeration	<ul style="list-style-type: none"> <li>• Continued cable pulling and terminations.</li> <li>• Continued pipe insulation.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue pipe insulation.</li> <li>• Continue installation of lighting.</li> <li>• Continue work on process systems to support the turnover skyline.</li> </ul>
Train 2	<ul style="list-style-type: none"> <li>• Completed initial lube oil flushes.</li> <li>• Completed installation of dry gas seals.</li> <li>• Continued steel erection.</li> <li>• Continued installation of aboveground pipe.</li> <li>• Commenced pipe insulation.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue installation of aboveground pipe and testing.</li> <li>• Continue pipe insulation.</li> <li>• Continue cable pulling and terminations to prepare for upcoming energization.</li> <li>• Commence preparation for turbine cold cranks.</li> </ul>
OSBL / Refrigerant Storage Area / Process Piperack	<ul style="list-style-type: none"> <li>• Continued concrete and steel activities.</li> <li>• Continued mechanical equipment activities.</li> <li>• Continued cable tray and conduit installation.</li> <li>• Continued cable pulling.</li> <li>• Continued loop checks.</li> <li>• Continued installation of lights and fixtures/devices.</li> <li>• Continued pipe insulation.</li> <li>• Continued installation of vapor barrier fence and light pole installation.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue installation of lighting.</li> <li>• Continue pipe insulation installation.</li> <li>• Continue with civil works.</li> </ul>
LNG Tank A	<ul style="list-style-type: none"> <li>• Continued logo painting.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue logo installation.</li> </ul>
LNG Tank C	<ul style="list-style-type: none"> <li>• Completed nitrogen purge.</li> <li>• Commenced preparation for logo painting.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue logo installation.</li> </ul>
Access Roads / Buildings	<ul style="list-style-type: none"> <li>• N/A</li> </ul>	<ul style="list-style-type: none"> <li>• N/A</li> </ul>
Marine Area	<ul style="list-style-type: none"> <li>• N/A</li> </ul>	<ul style="list-style-type: none"> <li>• N/A</li> </ul>

Corpus Christi Liquefaction, LLC  
November 2018 Monthly Progress Report

Area	Construction Activities in November	Planned Work for December
<b>(Stage 2 Project)</b>  ISBL and OSBL Train 3	<ul style="list-style-type: none"> <li>• Continued sitework, concrete and underground pipe activities.</li> <li>• Continued rebar and formwork.</li> <li>• Continued concrete placement.</li> <li>• Continued structural steel installation.</li> <li>• Continued installation of underground amine piping.</li> <li>• Continued double jointing of aboveground pipe.</li> <li>• Continued underground pipe testing activities.</li> <li>• Commenced installation of underground hot oil piping.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue mudmat placement.</li> <li>• Continue rebar and formwork activities.</li> <li>• Continue structural concrete placement.</li> <li>• Continue installation of grounding grid.</li> <li>• Continue installation of underground piping.</li> <li>• Continue structural steel installation.</li> <li>• Continue double jointing of aboveground pipe.</li> <li>• Continue loading aboveground piping.</li> </ul>
Tank B	<ul style="list-style-type: none"> <li>• Continued outer wall liner.</li> <li>• Continued rebar and formwork.</li> <li>• Continued roof panel assembly.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue rebar and formwork activities.</li> <li>• Continue outer wall liner work.</li> <li>• Commence roof panel assembly.</li> </ul>
Marine Area East Jetty Topside	<ul style="list-style-type: none"> <li>• N/A</li> </ul>	<ul style="list-style-type: none"> <li>• N/A</li> </ul>

## 6.0 Permitting and Environmental

No updates to any environmental permits or the Emergency Response Plan for project construction were made during the November reporting period.

### Summary of Problems, Non-Compliances, and Corrective Actions

Date	Description
N/A	

### Agency Contacts/Inspections

Agency	Name	Date	Location/Activity
N/A			

## 7.0 Progress Pictures



*Golar Tundra 1<sup>st</sup> ship at the West Jetty*



*Tank C west logo finish coat*

Corpus Christi Liquefaction, LLC  
November 2018 Monthly Progress Report



*Train 1 overview looking east*



*Train 2 overview looking northeast*



*Train 2 progress at propane refrigeration area*



*Tank B overview*

Corpus Christi Liquefaction, LLC  
November 2018 Monthly Progress Report



*Train 3 section 2 poured*



*Train 3 dehydration and mercury removal piperack erection*

Corpus Christi Liquefaction, LLC  
November 2018 Monthly Progress Report



*Train 3 installation of underground hot oil system piping*



*Tank B girder intermediate supports*

**CORPUS CHRISTI LIQUEFACTION PROJECT**

**Corpus Christi, Texas**

**MONTHLY PROGRESS REPORT  
DECEMBER 2018  
FERC DOCKET NO. CP12-507-000**

Corpus Christi Liquefaction, LLC  
December 2018 Monthly Progress Report

**Table of Contents**

1.0	Executive Summary .....	3
2.0	Project Highlights .....	3
3.0	Environmental, Safety, and Health Progress .....	3
4.0	Schedule .....	3
5.0	Construction .....	4
6.0	Permitting and Environmental .....	6
7.0	Progress Pictures .....	7

## 1.0 Executive Summary

This report covers activities for the CCL Stage 1 (Trains 1 and 2, Tanks A and C, OSBL, West Jetty and East Jetty Civil Works) and CCL Stage 2 (Train 3, Tank B and East Jetty Topsides) projects that occurred during the month of December 2018.

Stage 1 Engineering and Procurement are now 100.0% complete. Subcontract and direct hire construction work are 89.5% and 93.1% complete, respectively. Overall project completion for Stage 1 is 96.7%. Train 1 is projected to achieve substantial completion in the 1<sup>st</sup> half of 2019 and Train 2 in the 2<sup>nd</sup> half of 2019.

Stage 2 Engineering is 87.0% complete. Procurement is 63.0% complete. Subcontract and direct hire construction work are 8.5% and 11.7% complete, respectively. Overall project completion for Stage 2 is 42.0%.

## 2.0 Project Highlights

Stage 1 construction remains focused on completion of insulation of critical path systems. The team also continued to focus on pipe testing, restoration and pipe insulation. Major accomplishments in December included: successfully achieving first cargo from Train 1. Construction has turned 317 systems over to Startup through the end of December.

Stage 2 construction continued with site excavation, concrete placement, structural steel erection, underground piping, and aboveground piping activities. The team also placed the methane section of the compressor deck this month. Loading of above-ground pipe in the cryogenic and AGRU racks are also well underway.

## 3.0 Environmental, Safety, and Health Progress – Stage 1

	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>
Bechtel	10	734	14	1322	0	65	0	1
Subcontractor	0	0	0	0	0	0	0	2
Total	10	734	14	1322	0	65	0	3

1. ITD = Inception to Date.

## Environmental, Safety, and Health Progress – Stage 2

	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>
Bechtel	7	22	3	22	0	3	0	0
Subcontractor	0	0	0	0	0	0	0	0
Total	7	22	3	22	0	3	0	0

1. ITD = Inception to Date.

## 4.0 Schedule

Train 1 is projected to achieve substantial completion in the 1<sup>st</sup> half of 2019 and Train 2 in the 2<sup>nd</sup> half of 2019. Activities planned for the month of January 2019 are on track.

## 5.0 Construction

Area	Construction Activities in December	Planned Work for January
<b>(Stage 1 Project)</b>  ISBL Train 1 Compressor Area / Cryogenic Piperack / Propane Refrigeration	<ul style="list-style-type: none"> <li>• Continued cable pulling and terminations.</li> <li>• Continued pipe insulation.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue work on process systems to support turnover skyline.</li> <li>• Continue installation of lighting.</li> <li>• Complete pipe insulation.</li> </ul>
Train 2	<ul style="list-style-type: none"> <li>• Continued lube oil flushes.</li> <li>• Continued steel erection.</li> <li>• Continued installation of aboveground pipe.</li> <li>• Continued pipe insulation.</li> <li>• Continued cable pulling and terminations.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue installation of aboveground pipe and testing.</li> <li>• Continue pipe insulation.</li> <li>• Continue cable pulling and terminations to prepare for upcoming energization.</li> <li>• Commence preparation for compressor mechanical runs.</li> </ul>
OSBL / Refrigerant Storage Area / Process Piperack	<ul style="list-style-type: none"> <li>• Continued concrete and steel activities.</li> <li>• Continued mechanical equipment activities.</li> <li>• Continued cable tray and conduit installation.</li> <li>• Continued cable pulling.</li> <li>• Continued loop checks.</li> <li>• Continued installation of lights and fixtures/devices.</li> <li>• Continued pipe insulation.</li> <li>• Continued installation of plant fencing and light pole.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue installation of lighting.</li> <li>• Continue pipe insulation installation.</li> <li>• Continue with civil works.</li> </ul>
LNG Tank A	<ul style="list-style-type: none"> <li>• Continued logo painting.</li> <li>• Continued closing punchlist items.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue logo installation.</li> <li>• Continue closing punchlist items.</li> </ul>
LNG Tank C	<ul style="list-style-type: none"> <li>• Continued logo painting.</li> <li>• Continued closing punchlist items.</li> </ul>	<ul style="list-style-type: none"> <li>• Turnover to Cheniere.</li> </ul>
Access Roads / Buildings	<ul style="list-style-type: none"> <li>• N/A</li> </ul>	<ul style="list-style-type: none"> <li>• N/A</li> </ul>
Marine Area	<ul style="list-style-type: none"> <li>• N/A</li> </ul>	<ul style="list-style-type: none"> <li>• N/A</li> </ul>

Corpus Christi Liquefaction, LLC  
December 2018 Monthly Progress Report

Area	Construction Activities in December	Planned Work for January
<b>(Stage 2 Project)</b>  ISBL and OSBL Train 3	<ul style="list-style-type: none"> <li>• Continued sitework, concrete and underground pipe activities.</li> <li>• Continued concrete placement.</li> <li>• Continued structural steel installation.</li> <li>• Continued double jointing of aboveground pipe.</li> <li>• Completed installation of underground amine piping.</li> <li>• Completed installation of underground hot oil piping.</li> <li>• Completed installation of underground firewater piping.</li> <li>• Commenced installation of hockey sticks under propane compressor deck.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue concrete placements.</li> <li>• Continue installation of underground firewater piping.</li> <li>• Continue structural steel installation.</li> <li>• Continue double jointing of aboveground pipe.</li> <li>• Continue mudmat placement.</li> <li>• Continue loading aboveground piping.</li> <li>• Continue installation of hockey sticks under propane compressor deck.</li> </ul>
Tank B	<ul style="list-style-type: none"> <li>• Continued outer wall liner.</li> <li>• Continued rebar and formwork.</li> <li>• Commenced roof panel assembly.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue rebar and formwork activities.</li> <li>• Continue outer wall liner work.</li> <li>• Commence roof panel assembly.</li> </ul>
Marine Area East Jetty Topside	<ul style="list-style-type: none"> <li>• N/A</li> </ul>	<ul style="list-style-type: none"> <li>• N/A</li> </ul>

**6.0 Permitting and Environmental**

No updates to any environmental permits or the Emergency Response Plan for project construction were made during the December reporting period.

**Summary of Problems, Non-Compliances, and Corrective Actions**

Date	Description
N/A	

**Agency Contacts/Inspections**

Agency	Name	Date	Location/Activity
FERC	Steven Kusy Wimberly Hoogendoorn John Bugno	December 12 -13, 2018	Construction Inspection. No deficiencies noted.

## 7.0 Progress Pictures



*Stage 1 Area Paving and Final Grading in OSBL*



*Stage 1 – Tank A*

Corpus Christi Liquefaction, LLC  
December 2018 Monthly Progress Report



*Stage 1 Second Cargo Ship for Train 1*



*Stage 1 Train 1 Area Paving*

Corpus Christi Liquefaction, LLC  
December 2018 Monthly Progress Report



*Stage 1 Tank C West Logo Finish Coat*



*Stage 2 Train 3 Methane Deck Compressor Pads Poured*

Corpus Christi Liquefaction, LLC  
December 2018 Monthly Progress Report



*Stage 2 Tank B Overview*



*Stage 2 Train 3 Steel Installation*

Corpus Christi Liquefaction, LLC  
December 2018 Monthly Progress Report



*Stage 2 Tank B Roof Installation Progress*



*Stage 2 Train 3 Propane Refrigeration Trench Installation*

Corpus Christi Liquefaction, LLC  
December 2018 Monthly Progress Report



*Overview – Marine Facilities*

**CORPUS CHRISTI LIQUEFACTION PROJECT**

**Corpus Christi, Texas**

**MONTHLY PROGRESS REPORT  
JANUARY 2019  
FERC DOCKET NO. CP12-507-000**

Corpus Christi Liquefaction, LLC  
January 2019 Monthly Progress Report

**Table of Contents**

1.0	Executive Summary .....	3
2.0	Project Highlights .....	3
3.0	Environmental, Safety, and Health Progress .....	3
4.0	Schedule .....	3
5.0	Construction .....	4
6.0	Permitting and Environmental .....	6
7.0	Progress Pictures .....	7

## 1.0 Executive Summary

This report covers activities for the CCL Stage 1 (Trains 1 and 2, Tanks A and C, OSBL, West Jetty and East Jetty Civil Works) and CCL Stage 2 (Train 3, Tank B and East Jetty Topsides) projects that occurred during the month of January 2019.

Stage 1 Engineering and Procurement are now 100.0% complete. Subcontract and direct hire construction work are 89.9% and 94.5% complete, respectively. Overall project completion for Stage 1 is 97.3%. Train 1 is projected to achieve substantial completion in the 1<sup>st</sup> half of 2019 and Train 2 in the 2<sup>nd</sup> half of 2019.

Stage 2 Engineering is 89.2% complete. Procurement is 65.2% complete. Subcontract and direct hire construction work are 8.9% and 13.5% complete, respectively. Overall project completion for Stage 2 is 43.9%.

## 2.0 Project Highlights

Stage 1 construction remains focused on completing strainer shutdown work in Train 1 and completion of remaining insulation and punchlist items. Preparations for the performance test also commenced. The team also continued to focus on pipe testing, restoration and pipe insulation, and preparation for first fuel gas and compressor mechanical runs. Construction has turned 327 systems over to Startup through the end of January.

Stage 2 construction has completed the majority of the concrete foundation work and underground pipe installation. Construction continued to progress Train 3 sitework, concrete pedestals/paving, structural steel erection, and aboveground piping activities. Loading of aboveground pipe in the cryogenic rack, AGRU rack, and propane condenser rack are also well underway. Cable tray installation commenced at the cryo and propane condenser rack. LNG Tank B continued the installation of the outer wall liner and roof panels. Piping and steel installation at the East Jetty also commenced in January.

## 3.0 Environmental, Safety, and Health Progress – Stage 1

	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>
Bechtel	5	739	20	1342	1	66	0	1
Subcontractor	0	0	0	0	0	0	0	2
<b>Total</b>	<b>5</b>	<b>739</b>	<b>20</b>	<b>1342</b>	<b>1</b>	<b>66</b>	<b>0</b>	<b>3</b>

1. ITD = Inception to Date.

### Environmental, Safety, and Health Progress – Stage 2

	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>
Bechtel	5	27	4	26	0	3	0	0
Subcontractor	0	0	0	0	0	0	0	0
<b>Total</b>	<b>5</b>	<b>27</b>	<b>4</b>	<b>26</b>	<b>0</b>	<b>3</b>	<b>0</b>	<b>0</b>

1. ITD = Inception to Date.

## 4.0 Schedule

Train 1 is projected to achieve substantial completion in the 1<sup>st</sup> half of 2019 and Train 2 in the 2<sup>nd</sup> half of 2019. Activities planned for the month of February 2019 are on track.

Corpus Christi Liquefaction, LLC  
January 2019 Monthly Progress Report

**5.0 Construction**

Area	Construction Activities in January	Planned Work for February
<b>(Stage 1 Project)</b>  ISBL Train 1 Compressor Area / Cryogenic Piperack / Propane Refrigeration	<ul style="list-style-type: none"> <li>• Continued pipe insulation.</li> <li>• Continued installation of lighting.</li> </ul>	<ul style="list-style-type: none"> <li>• Complete installation of lighting and fixtures.</li> <li>• Turnover Care Custody and Control (TCCC) to Cheniere.</li> </ul>
Train 2	<ul style="list-style-type: none"> <li>• Continued installation of aboveground pipe and testing.</li> <li>• Continued pipe insulation.</li> <li>• Continued cable pulling and terminations.</li> <li>• Completed chemical flush.</li> <li>• Prepared for compressor mechanical runs.</li> </ul>	<ul style="list-style-type: none"> <li>• Complete perlite loading of the Ethylene Cold Box.</li> <li>• Continue installation of aboveground pipe, testing and restoration.</li> <li>• Continue pipe insulation.</li> <li>• Continue cable pulling and terminations.</li> <li>• Commence preparation for compressor mechanical runs.</li> </ul>
OSBL / Refrigerant Storage Area / Process Piperack	<ul style="list-style-type: none"> <li>• Continued installation of lights and fixtures/devices.</li> <li>• Continued pipe insulation punchlist.</li> <li>• Continued installation of plant fencing and light pole installation.</li> <li>• Continued final grading, area paving, and asphalt work.</li> </ul>	<ul style="list-style-type: none"> <li>• Complete installation of lighting.</li> <li>• Complete pipe insulation punchlist.</li> <li>• Continue with final grading, area paving, and asphalt work.</li> </ul>
LNG Tank A	<ul style="list-style-type: none"> <li>• Continued logo painting.</li> <li>• Continued closing punchlist items.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue logo installation.</li> <li>• Continue closing punchlist items.</li> </ul>
LNG Tank C	<ul style="list-style-type: none"> <li>• Continued logo painting.</li> <li>• Continued closing punchlist items.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue logo installation.</li> <li>• Continue closing punchlist items.</li> </ul>
Access Roads / Buildings	<ul style="list-style-type: none"> <li>• N/A</li> </ul>	<ul style="list-style-type: none"> <li>• N/A</li> </ul>
Marine Area	<ul style="list-style-type: none"> <li>• N/A</li> </ul>	<ul style="list-style-type: none"> <li>• N/A</li> </ul>

Corpus Christi Liquefaction, LLC  
January 2019 Monthly Progress Report

Area	Construction Activities in January	Planned Work for February
<b>(Stage 2 Project)</b>  ISBL and OSBL Train 3	<ul style="list-style-type: none"> <li>• Continued sitework, concrete and underground pipe activities.</li> <li>• Continued installation of underground firewater piping.</li> <li>• Continued structural steel installation.</li> <li>• Continued double jointing of aboveground pipe.</li> <li>• Continued installation of hockey sticks under compressor deck.</li> <li>• Commenced cable tray installation.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue concrete placements.</li> <li>• Continue installation of underground firewater piping.</li> <li>• Continue structural steel installation.</li> <li>• Continue double jointing of aboveground pipe.</li> <li>• Continue loading aboveground piping.</li> <li>• Continue installation of hockey sticks under compressor deck.</li> <li>• Continue cable tray installation.</li> </ul>
Tank B	<ul style="list-style-type: none"> <li>• Continued outer wall liner.</li> <li>• Continued rebar and formwork.</li> <li>• Continued roof panel assembly.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue rebar and formwork activities.</li> <li>• Continue outer wall liner work.</li> <li>• Continue roof panel assembly.</li> </ul>
Marine Area East Jetty Topside	<ul style="list-style-type: none"> <li>• N/A</li> </ul>	<ul style="list-style-type: none"> <li>• N/A</li> </ul>

## 6.0 Permitting and Environmental

No updates to any environmental permits or the Emergency Response Plan for project construction were made during the January reporting period.

### Summary of Problems, Non-Compliances, and Corrective Actions

Date	Description
N/A	

### Agency Contacts/Inspections

Agency	Name	Date	Location/Activity
N/A			

## 7.0 Progress Pictures



Stage 1 OSBL West Jetty and Marine Flare



Stage 1 West and East jetty overview

Corpus Christi Liquefaction, LLC  
January 2019 Monthly Progress Report



*Marine East Berth*



*LNG Storage Tanks – A, B, & C*



*Stage 1 Tank C Logo Installation*




*Stage 2 Pipe installation commenced at East jetty*

Corpus Christi Liquefaction, LLC  
January 2019 Monthly Progress Report



*Stage 2 East jetty trestles*

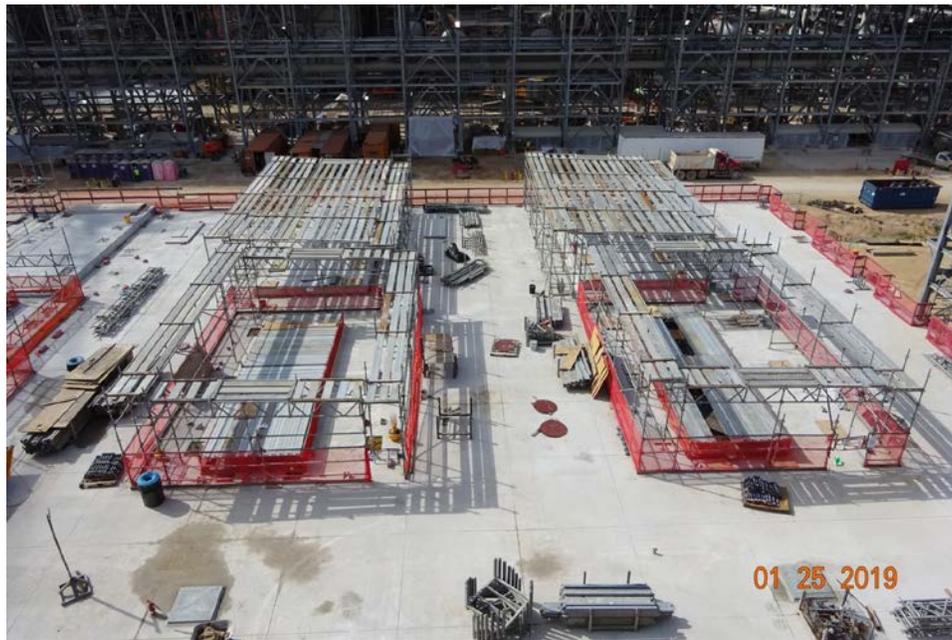

*Stage 2 Compressor Deck*

**CORPUS CHRISTI LIQUEFACTION PROJECT**

**Corpus Christi, Texas**

**MONTHLY PROGRESS REPORT  
FEBRUARY 2019  
FERC DOCKET NO. CP12-507-000**

Corpus Christi Liquefaction, LLC  
February 2019 Monthly Progress Report

**Table of Contents**

1.0	Executive Summary .....	3
2.0	Project Highlights .....	3
3.0	Environmental, Safety, and Health Progress .....	3
4.0	Schedule .....	3
5.0	Construction .....	4
6.0	Permitting and Environmental .....	6
7.0	Progress Pictures .....	7

## 1.0 Executive Summary

This report covers activities for the CCL Stage 1 (Trains 1 and 2, Tanks A and C, OSBL, West Jetty and East Jetty Civil Works) and CCL Stage 2 (Train 3, Tank B and East Jetty Topsides) projects that occurred during the month of February 2019.

Stage 1 Engineering and Procurement are now 100.0% complete. Subcontract and direct hire construction work are 91.7% and 95.4% complete, respectively. Overall project completion for Stage 1 is 97.8%.

Stage 2 Engineering is 90.0% complete. Procurement is 75.3% complete. Subcontract and direct hire construction work are 9.8% and 16.6% complete, respectively. Overall project completion for Stage 2 is 49.7%.

Train 1 substantial completion was achieved on February 28, 2019. Actual project progress supports the achievement of substantial completion for Train 2 in the second half of 2019.

## 2.0 Project Highlights

Stage 1 engineering and procurement disciplines are complete. The remaining engineering effort focuses on construction and CSU support and documentation close-out. Construction continued to focus on pipe testing, restoration, pipe insulation and compressor mechanical runs. Construction has turned 348 systems over to Startup through the end of February.

Stage 2 engineering disciplines are substantially complete. Construction continued with placement of concrete foundations, aboveground piping installation, steel erection, and cable tray installation. LNG Tank B concrete wall pours and roof panel assembly continued to progress. The team commenced mechanical equipment installation in Train 3 with the setting of the feed gas heater and aboveground piping installation continued at the East Jetty.

## 3.0 Environmental, Safety, and Health Progress – Stage 1

	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>
Bechtel	12	751	17	1359	0	66	0	1
Subcontractor	0	0	0	0	0	0	0	2
Total	12	751	17	1359	0	66	0	3

1. ITD = Inception to Date.

## Environmental, Safety, and Health Progress – Stage 2

	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>	Month	ITD <sup>1</sup>
Bechtel	3	30	3	29	0	3	0	0
Subcontractor	0	0	0	0	0	0	0	0
Total	3	30	3	29	0	3	0	0

1. ITD = Inception to Date.

## 4.0 Schedule

Train 1 achieved substantial completion on February 28, 2019. Train 2 is projected to achieve substantial completion in the 2<sup>nd</sup> half of 2019. Activities planned for the month of March 2019 are on track.

Corpus Christi Liquefaction, LLC  
February 2019 Monthly Progress Report

**5.0 Construction**

Area	Construction Activities in February	Planned Work for March
<b>(Stage 1 Project)</b>  ISBL Train 1 Compressor Area / Cryogenic Piperack / Propane Refrigeration	<ul style="list-style-type: none"> <li>• Issued the request to Turnover Care, Custody, and Control ("TCCC") .</li> </ul>	<ul style="list-style-type: none"> <li>• Continue closing TCCC exceptions.</li> <li>• Continue to complete and turnover systems to CSU for Train 2.</li> </ul>
Train 2	<ul style="list-style-type: none"> <li>• Completed perlite loading of the ethylene cold box.</li> <li>• Continued installation of aboveground pipe and testing.</li> <li>• Continued pipe insulation.</li> <li>• Continued cable pulling and terminations.</li> <li>• Commenced compressor mechanical runs.</li> </ul>	<ul style="list-style-type: none"> <li>• Complete perlite loading of the Methane Cold Box.</li> <li>• Continue installation of aboveground pipe, testing and restoration.</li> <li>• Continue pipe insulation.</li> <li>• Continue cable pulling and terminations.</li> <li>• Complete compressor mechanical runs.</li> </ul>
OSBL / Refrigerant Storage Area / Process Piperack	<ul style="list-style-type: none"> <li>• Continued installation of lights and fixtures/devices.</li> <li>• Continued pipe insulation punchlist.</li> <li>• Continued installation of plant fencing and light pole installation.</li> <li>• Continued final grading, area paving, and asphalt work.</li> <li>• Completed TCCC of OSBL.</li> </ul>	<ul style="list-style-type: none"> <li>• Complete installation of lighting.</li> <li>• Continue with final grading, area paving, and asphalt work.</li> </ul>
LNG Tank A	<ul style="list-style-type: none"> <li>• Continued closing punchlist items.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue closing punchlist items.</li> </ul>
LNG Tank C	<ul style="list-style-type: none"> <li>• Continued closing punchlist items.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue closing punchlist items.</li> </ul>
Access Roads / Buildings	<ul style="list-style-type: none"> <li>• N/A</li> </ul>	<ul style="list-style-type: none"> <li>• N/A</li> </ul>
Marine Area	<ul style="list-style-type: none"> <li>• N/A</li> </ul>	<ul style="list-style-type: none"> <li>• N/A</li> </ul>

Corpus Christi Liquefaction, LLC  
February 2019 Monthly Progress Report

Area	Construction Activities in February	Planned Work for March
<b>(Stage 2 Project)</b>  ISBL and OSBL Train 3	<ul style="list-style-type: none"> <li>• Continued sitework and concrete activities.</li> <li>• Continued structural steel installation.</li> <li>• Continued pipe loading.</li> <li>• Continued cable tray installation.</li> <li>• Continued installation of hockey sticks under compressor deck.</li> <li>• Commenced mechanical equipment setting.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue concrete placements.</li> <li>• Continue structural steel installation.</li> <li>• Continue aboveground piping activities.</li> <li>• Continue mechanical equipment setting.</li> <li>• Continue cable tray installation.</li> </ul>
Tank B	<ul style="list-style-type: none"> <li>• Continued outer wall liner.</li> <li>• Continued rebar and formwork.</li> <li>• Continued roof panel assembly.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue rebar and formwork activities.</li> <li>• Continue outer wall liner work.</li> <li>• Continue roof panel assembly.</li> </ul>
Marine Area East Jetty Topside	<ul style="list-style-type: none"> <li>• Commence aboveground pipe installation.</li> </ul>	<ul style="list-style-type: none"> <li>• Continue aboveground pipe installation.</li> </ul>

## 6.0 Permitting and Environmental

No updates to any environmental permits or the Emergency Response Plan for project construction were made during the February reporting period.

### Summary of Problems, Non-Compliances, and Corrective Actions

Date	Description
N/A	


### Agency Contacts/Inspections

Agency	Name	Date	Location/Activity
FERC	Steven Kusy Wimberly Hoogendoorn	February 6, 2019	Construction Inspection. No deficiencies noted.

## 7.0 Progress Pictures



Train 1 at TCCC

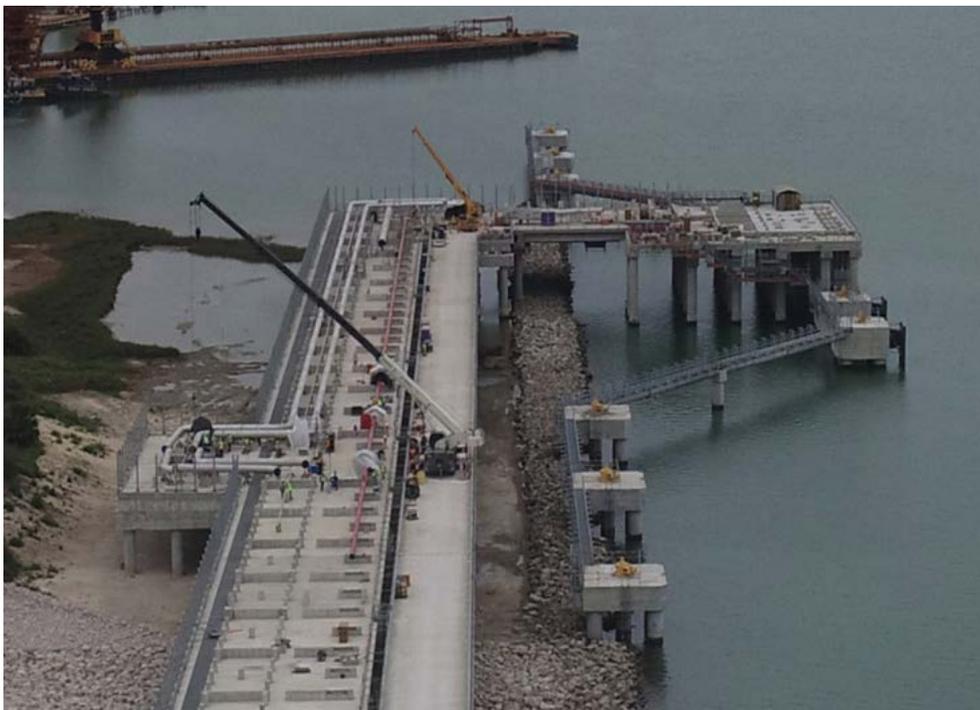

East Jetty piping progress

Corpus Christi Liquefaction, LLC  
February 2019 Monthly Progress Report



Train 2 area overview progress



Train 2 Perlite loading to Ethylene Cold Box progress



Tank C West Logo



East Jetty Aboveground Piping Installation

Corpus Christi Liquefaction, LLC  
February 2019 Monthly Progress Report



Refrigeration Compressor Area Overview



LNG Tank B Construction
