



Cheniere Energy, Inc.
845 Texas Avenue, Suite 1250
Houston, Texas 77002
phone: 713.375.5000
fax: 713.375.6000

RECEIVED

By Docket Room at 8:13 am, Oct 01, 2026

September 30, 2026

Submitted Via DOE's Online Portal

Ms. Amy Sweeney, Director
Office of Global Energy Security
Hydrocarbons and Geothermal Energy Office
Forrestal Building, FE-34
1000 Independence Ave. S.W.
Washington, D.C. 20585

Re: DOE Semi-Annual Report for Period of March 1, 2026 through August 31, 2026
Cheniere Marketing, LLC and Corpus Christi Liquefaction, LLC
HGEO Docket Nos. / Orders:

- 12-97-LNG / 3638
- 12-99-LNG / 3164
- 19-124-LNG / 4519 & 4799

Corpus Christi Liquefaction, LLC (as successor to Corpus Christi Liquefaction Stage III, LLC & Corpus Christi Liquefaction Stage IV, LLC)
HGEO Docket Nos. / Orders:

- 18-78-LNG / 4277 & 4490

Corpus Christi Liquefaction, LLC; CCL Midscale 8-9, LLC and Cheniere Marketing, LLC
HGEO Docket Nos. / Orders:

- 23-46-LNG / 5019 & 5391

Corpus Christi Liquefaction, LLC; Corpus Christi Liquefaction Stage IV, LLC; and Cheniere Marketing, LLC
HGEO Docket Nos. / Orders:

- 26-32-LNG / 5454

Pursuant to the above-referenced Orders, Cheniere Marketing, LLC ("CMLLC"), Corpus Christi Liquefaction, LLC ("CCL"), CCL Midscale 8-9, LLC ("CCL Midscale"), and Corpus Christi Liquefaction Stage IV, LLC herein submit the semi-annual report for March 1, 2026 through August 31, 2026. This report includes a list of the items which have been filed during the reporting period relating to long-term contracts associated with the long-term export of LNG from the Corpus Christi LNG Terminal, as well as long-term gas supply contracts. Additionally, provided as **Attachment A** are the construction reports for the Corpus Christi Liquefaction Stage 3 Project and Corpus Christi Liquefaction Midscale Trains 8 & 9 Project that have been provided to the Federal Energy Regulatory Commission in Docket Nos. CP18-512-000 and CP23-129-000, respectively, covering the reporting period.

- CMLLC, CCL, and CCL Midscale submitted the following long-term contract(s) associated with the long-term export of LNG from the Corpus Christi LNG Terminal during the reporting period:

- CCL entered into a Deed of Termination of the Orlen S.A. LNG Sale and Purchase Agreement.
 - On April 17, 2026, CMLLC, CCL, and ENN LNG (Singapore) Pte. Ltd. ("ENN") entered into a Novation and Amendment Agreement, which amends and assigns to CCL the previously submitted LNG sale and purchase agreement entered into by CMLLC and ENN on June 26, 2023.
 - On June 26, 2026, CMLLC, Sabine Pass Liquefaction, LLC ("SPL"), and Equinor ASA entered into a Novation and Amendment Agreement, which amends and assigns to SPL the previously submitted LNG sale and purchase agreement entered into by CMLLC and Equinor ASA on June 8, 2022.
 - On July 1, 2026, CMLLC, SPL, and PetroChina International Company Limited entered into a Novation and Amendment Deed, which amends and assigns to Sabine Pass Liquefaction, LLC the previously submitted LNG sale and purchase agreement entered into by CMLLC and PetroChina International Company Limited on July 15, 2022.
 - On August 3, 2026, CCL entered into a Novation and Amendment Agreement which assigns the SPA dated May 30, 2014 between CCL and Iberdrola Energia España, S.A.U. (formerly Iberdrola Generacion Espana S.A.U.) ("Iberdrola") from Iberdrola to Shell International Trading Middle East Limited FZE.
 - On August 4, 2026, CCL entered into a LNG SPA with Cheniere Marketing International LLP for an aggregated annual contract quantity of approximately 44,000,000 MMBtus.
- CMLLC, CCL, and CCL Midscale submitted the following long-term gas supply contract(s) during the reporting period:
 - On April 24, 2026, CCL entered into a Transaction Confirmation with Pioneer Natural Resources USA, Inc., governed by that certain NAESB Base Contract for Sale and Purchase of Natural Gas dated June 1, 2015, for an aggregated annual contract quantity of approximately 55,000,000 MMBtus.
 - On June 26, 2026, CMLLC, CCL, and Cannat Energy Inc., entered into the Assignment, Assumption, Consent and Amendment Agreement, which amends and assigns to CCL the previously submitted Gas Supply Agreement entered into by CMLLC and Cannat Energy Inc. on March 27, 2025

Should you have any questions about the instant filing, please feel free to contact the undersigned at (713) 375-5000.

Respectfully,



Karri Mahmoud
 Cheniere Marketing, LLC
 Corpus Christi Liquefaction, LLC
 CCL Midscale 8-9, LLC
 Corpus Christi Liquefaction Stage IV, LLC

ATTACHMENT A

**CORPUS CHRISTI LIQUEFACTION STAGE 3 PROJECT
CORPUS CHRISTI LIQUEFACTION MIDSCALE TRAINS 8 & 9 PROJECT**

Corpus Christi, Texas

**MONTHLY PROGRESS REPORT
MARCH 2026**

**FERC DOCKET NO. CP18-512-000 (STAGE 3)
FERC DOCKET NO. CP23-129-000 (TRAINS 8 & 9)**

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
March 2026 Monthly Progress Report

Table of Contents

1.0	Executive Summary	3
2.0	Project Highlights	3
3.0	Environmental, Safety, and Health Progress	3
4.0	Schedule	4
5.0	Construction	5
6.0	Permitting and Environmental	8
7.0	Progress Photos.....	9

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
March 2026 Monthly Progress Report

1.0 Executive Summary

On November 22, 2019, the Federal Energy Regulatory Commission (“FERC” or “Commission”) issued an Order Issuing Authority Under Section 3 and Section 7(c) of the Natural Gas Act (“NGA”) (“Order”) granting the necessary authorization to Corpus Christi Liquefaction (“CCL”) for the construction and operation of an expansion of the Corpus Christi Liquefaction Project (“Stage 3 Project”). On March 10, 2025, the FERC issued an Order granting the necessary authorization to CCL for the construction and operation of a second expansion of the Corpus Christi Liquefaction Project (“Midscale Trains 8 & 9 Project”). This report covers activities for the Stage 3 Project and the Midscale Trains 8 & 9 Project during the month of March 2026.

The Stage 3 Project Engineering and Procurement are 99.7% and 100% complete, respectively. Subcontract and direct hire construction work are 96.8% and 91.0% complete, respectively. Overall project completion for the Stage 3 Project is 96.5%.

The Trains 8 & 9 Project Engineering and Procurement are 85.8% and 51.7%, respectively. Subcontract and direct hire construction work are 41.3% and 2.5% complete, respectively. Overall project completion for the Trains 8 & 9 Project is 36.9%.

2.0 Project Highlights

Key work fronts for the Stage 3 Project included aboveground piping in Train 6 - 7 and outside boundary limits (“OSBL”), concrete pours in Trains 6 – 7 and OSBL, structural steel erection in Trains 6 - 7 and OSBL, and underground piping installation in OSBL. Additional continued work includes road improvements, drainage work, and mobilization of temporary facilities, equipment, and personnel.

Key work fronts for the Midscale Trains 8 & 9 Project included pile installations, excavations, concrete pours, underground piping installation, and structural steel installation.

3.0 Environmental, Safety, and Health Progress

The following table includes health and safety incidents for the Stage 3 Project.

Stage 3 Project								
	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹
Bechtel	22	1,189	30	1,299	0	26	0	2
Subcontractor	0	92	0	22	0	2	0	0
Total	22	1,281	30	1,321	0	28	0	2

1. ITD = Inception to Date.

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
March 2026 Monthly Progress Report

The following table includes health and safety incidents for the Midscale Trains 8 & 9 Project.

Midscale Trains 8 & 9 Project								
	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹
Bechtel	0	4	1	3	0	0	0	0
Subcontractor	0	1	0	3	0	0	0	0
Total	0	5	1	6	0	0	0	0

1. ITD = Inception to Date.

4.0 Schedule

There were no changes to the Stage 3 Project schedule during the reporting period. An additional schedule for the Midscale Trains 8 & 9 Project was provided on April 10, 2025 (Accession No. 202504105188).

5.0 Emergency Response Plan Updates

There were no updates to the Emergency Response Plan for the reporting period. The table below identifies the emergency response committee meetings for 2026.

2026 Committee Meetings		
CCLEPC	STWAC	CPLEPC
January 6, 2026	January 15, 2026	February 19, 2026
March 3, 2026	April 16, 2026	May 21, 2026
May 5, 2026	July 16, 2026	August 20, 2026
July 7, 2026	August 15, 2026	November 19, 2026
September 1, 2026		
November 3, 2026		

Please refer to the following websites for additional information on the emergency response organizations:

- <https://coastalplainlepc.org/>
- <https://www.stwac.org/>
- <https://cclepc.org/wpbuild/>

Additionally, the Port of Corpus Christi (POCC) conducted and facilitated a drill with POCC local and regional stakeholders on a tugboat event alongside a docked LNG vessel. CCL participated in the event as a POCC stakeholder.

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
March 2026 Monthly Progress Report

6.0 Construction

The following table includes current and planned construction activities for the Stage 3 Project.

Stage 3 Project		
Area	Construction Activities in Current Month	Planned Work for Next Month
Liquefaction Train 5	- Completed concrete foundation and pedestal works - Continued insulation of aboveground piping	- Complete insulation of aboveground piping - Substantial completion
Liquefaction Train 6	- Continued excavation to support the upcoming concrete pours - Continued concrete foundations and pedestal works - Continued installation of structural steel - Continued installation of aboveground piping - Continued insulation of aboveground piping - Continued cable pulls	- Continue excavation to support the upcoming concrete pours - Continue concrete foundations and pedestal works - Continue installation of structural steel - Continue installation of aboveground piping - Continue insulation of aboveground piping - Continue cable pulls
Liquefaction Train 7	- Continued excavation to support the upcoming concrete pours - Continued concrete foundation and pedestal works - Continued installation of structural steel - Continued installation of aboveground piping - Continued cable pulls	- Continue excavation to support the upcoming concrete pours - Continue concrete foundation and pedestal works - Continue installation of structural steel - Continue installation of aboveground piping - Continue cable pulls
OSBL Area East/West/South	- Continued drainage works at OSBL East and South - Continued installation of reinforced concrete box culverts drains in OSBL East area - Continued excavations in OSBL East and South - Continued concrete foundations and pedestal works in OSBL West and Phase 2 areas - Continued installation of structural steel in OSBL West and South areas - Continued testing of underground piping - Continued installation and testing of aboveground piping - Continued installation of electrical duct banks in OSBL East, West and South areas - Continued cable pulls	- Continue drainage works in OSBL East and South - Continue installation of reinforced concrete box culvert drains in OSBL East area - Continue excavations in OSBL East and South - Continue concrete foundations and pedestal works - Continue installation of structural steel - Continue testing of underground piping - Continue installation and testing of aboveground piping - Continue installation of electrical duct banks - Continue cable pulls

Corpus Christi Liquefaction Stage 3 Project
 Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
 March 2026 Monthly Progress Report

Stage 3 Project		
Area	Construction Activities in Current Month	Planned Work for Next Month
Access Roads / Buildings / Other	- Continued road improvements and drainage work - Completed asphalt work in Train 4 <u>O&M Buildings & Welcome Center:</u> - Continued electrical and plumbing work - Continued installation of metal panels and floor - Continued paving striping - Continued landscaping	- Continue road improvements and drainage work <u>O&M Buildings & Welcome Center:</u> - Continue electrical and plumbing work - Continue installation of metal panels and floor - Continue paving striping - Continue landscaping

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
March 2026 Monthly Progress Report

The following table includes current and planned construction activities for the Midscale Trains 8 & 9 Project.

Midscale Trains 8 & 9 Project		
Area	Construction Activities in Current Month	Planned Work for Next Month
Liquefaction Train 8	- Continued excavation activities - Continued concrete pours for foundations - Continued installation of underground piping - Commenced installation of structural steel	- Continue excavation activities - Continue concrete pours for foundations - Continue installation of underground piping - Commence installation of electrical duct banks - Continue installation of structural steel
Liquefaction Train 9	- Commenced excavation activities - Commenced concrete pours for foundations	- Continue excavation activities - Continue concrete pours for foundations
EFG	- Continued excavation activities - Continued installation of underground piping	- Continue excavation activities - Commence concrete pours for foundations - Continue installation of underground piping
Refrigerant Storage	Continued piling installations	Continue piling installations
Access Roads/Other	Continued construction of heavy haul road	Continue construction of heavy haul road

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
March 2026 Monthly Progress Report

7.0 Permitting and Environmental

Summary of Problems, Non-Compliances, and Corrective Actions

Date	Description
December 16, 2025	A problem area was identified during the December 16, 2026, FERC environmental inspection. The FERC inspection report is available under FERC Accession No. 20251230-3013. The identified problem area has been corrected.

Agency Contacts/Inspections

Agency	Name	Date	Location/Activity
None.			

8.0 Progress Photos



Photo 1: Train 7 Aboveground Piping Installation



Photo 2: Train 8 Liquefaction Substation Foundation

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
March 2026 Monthly Progress Report



Photo 3: Train 8 Cryogenic Rack Foundation



Photo 4: Train 8 Structural Steel

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
March 2026 Monthly Progress Report



Photo 5: Refrigerant Storage Piling Installations

**CORPUS CHRISTI LIQUEFACTION STAGE 3 PROJECT
CORPUS CHRISTI LIQUEFACTION MIDSCALE TRAINS 8 & 9 PROJECT**

Corpus Christi, Texas

**MONTHLY PROGRESS REPORT
APRIL 2026**

**FERC DOCKET NO. CP18-512-000 (STAGE 3)
FERC DOCKET NO. CP23-129-000 (TRAINS 8 & 9)**

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
April 2026 Monthly Progress Report

Table of Contents

1.0	Executive Summary	3
2.0	Project Highlights	3
3.0	Environmental, Safety, and Health Progress	3
4.0	Schedule	4
5.0	Construction	5
6.0	Permitting and Environmental	8
7.0	Progress Photos.....	9

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
April 2026 Monthly Progress Report

1.0 Executive Summary

On November 22, 2019, the Federal Energy Regulatory Commission (“FERC” or “Commission”) issued an Order Issuing Authority Under Section 3 and Section 7(c) of the Natural Gas Act (“NGA”) (“Order”) granting the necessary authorization to Corpus Christi Liquefaction (“CCL”) for the construction and operation of an expansion of the Corpus Christi Liquefaction Project (“Stage 3 Project”). On March 10, 2025, the FERC issued an Order granting the necessary authorization to CCL for the construction and operation of a second expansion of the Corpus Christi Liquefaction Project (“Midscale Trains 8 & 9 Project”). This report covers activities for the Stage 3 Project and the Midscale Trains 8 & 9 Project during the month of April 2026.

The Stage 3 Project Engineering and Procurement are 99.7% and 100% complete, respectively. Subcontract and direct hire construction work are 97.5% and 93.3% complete, respectively. Overall project completion for the Stage 3 Project is 97.4%.

The Trains 8 & 9 Project Engineering and Procurement are 88.3% and 52.9%, respectively. Subcontract and direct hire construction work are 47.4% and 4.4% complete, respectively. Overall project completion for the Trains 8 & 9 Project is 38.9%.

2.0 Project Highlights

Key work fronts for the Stage 3 Project included aboveground piping in Train 6 - 7 and outside boundary limits (“OSBL”), concrete pours in Trains 6 – 7 and OSBL, structural steel erection in Trains 6 - 7 and OSBL, and underground piping installation in OSBL. Additional continued work includes road improvements, drainage work, and mobilization of temporary facilities, equipment, and personnel.

Key work fronts for the Midscale Trains 8 & 9 Project included pile installations, excavations, concrete pours, underground piping installation, and structural steel installation.

3.0 Environmental, Safety, and Health Progress

The following table includes health and safety incidents for the Stage 3 Project.

Stage 3 Project								
	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹
Bechtel	21	1,210	31	1,330	0	26	0	2
Subcontractor	1	93	0	22	0	2	0	0
Total	22	1,303	31	1,352	0	28	0	2

1. ITD = Inception to Date.

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
April 2026 Monthly Progress Report

The following table includes health and safety incidents for the Midscale Trains 8 & 9 Project.

Midscale Trains 8 & 9 Project								
	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹
Bechtel	3	7	6	9	0	0	0	0
Subcontractor	0	1	0	3	0	0	0	0
Total	3	8	6	12	0	0	0	0

1. ITD = Inception to Date.

4.0 Schedule

There were no changes to the Stage 3 Project schedule during the reporting period. An additional schedule for the Midscale Trains 8 & 9 Project was provided on April 10, 2025 (Accession No. 202504105188).

5.0 Emergency Response Plan Updates

There were no updates to the Emergency Response Plan for the reporting period. The table below identifies the emergency response committee meetings for 2026.

2026 Committee Meetings		
CCLEPC	STWAC	CPLEPC
January 6, 2026	January 15, 2026	February 19, 2026
March 3, 2026	April 16, 2026	May 21, 2026
May 5, 2026	July 16, 2026	August 20, 2026
July 7, 2026	August 15, 2026	November 19, 2026
September 1, 2026		
November 3, 2026		

Please refer to the following websites for additional information on the emergency response organizations:

- <https://coastalplainlepc.org/>
- <https://www.stwac.org/>
- <https://cclepc.org/wpbuild/>

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
April 2026 Monthly Progress Report

6.0 Construction

The following table includes current and planned construction activities for the Stage 3 Project.

Stage 3 Project		
Area	Construction Activities in Current Month	Planned Work for Next Month
Liquefaction Train 5	- Completed insulation of aboveground piping - Substantial completion	
Liquefaction Train 6	- Continued excavation to support the upcoming concrete pours - Continued concrete foundations and pedestal works - Continued installation of structural steel - Continued installation of aboveground piping - Continued insulation of aboveground piping - Continued cable pulls	- Continue excavation to support the upcoming concrete pours - Continue concrete foundations and pedestal works - Continue installation of structural steel - Continue installation of aboveground piping - Continue insulation of aboveground piping - Continue cable pulls
Liquefaction Train 7	- Continued excavation to support the upcoming concrete pours - Continued concrete foundation and pedestal works - Continued installation of structural steel - Continued installation of aboveground piping - Continued insulation of aboveground piping - Continued cable pulls	- Continue excavation to support the upcoming concrete pours - Continue concrete foundation and pedestal works - Continue installation of structural steel - Continue installation of aboveground piping - Continue insulation of aboveground piping - Continue cable pulls
OSBL Area East/West/South	- Continued drainage works at OSBL East and South - Continued installation of reinforced concrete box culverts drains in OSBL East area - Continued excavations in OSBL East and South - Continued concrete foundations and pedestal works in OSBL Phase 2 area - Continued installation of structural steel in OSBL West and South areas - Continued testing of underground piping - Continued installation and testing of aboveground piping - Continued installation of electrical duct banks in OSBL East, West and South areas - Continued cable pulls	- Continue drainage works in OSBL East and South - Continue installation of reinforced concrete box culvert drains in OSBL East area - Continue excavations in OSBL East and South - Continue concrete foundations and pedestal works - Continue installation of structural steel - Continue testing of underground piping - Continue installation and testing of aboveground piping - Continue installation of electrical duct banks - Continue cable pulls

Corpus Christi Liquefaction Stage 3 Project
 Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
 April 2026 Monthly Progress Report

Stage 3 Project		
Area	Construction Activities in Current Month	Planned Work for Next Month
Access Roads / Buildings / Other	- Continued road improvements and drainage work <u>O&M Buildings & Welcome Center:</u> - Continued electrical and plumbing work - Continued installation of metal panels and floor - Continued landscaping	- Continue road improvements and drainage work <u>O&M Buildings & Welcome Center:</u> - Continue electrical and plumbing work - Continue installation of metal panels and floor - Continue landscaping

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
April 2026 Monthly Progress Report

The following table includes current and planned construction activities for the Midscale Trains 8 & 9 Project.

Midscale Trains 8 & 9 Project		
Area	Construction Activities in Current Month	Planned Work for Next Month
Liquefaction Train 8	- Continued excavation activities - Continued concrete pours for foundations - Continued installation of underground piping - Continued installation of structural steel - Commenced installation of electrical duct banks	- Continue excavation activities - Continue concrete pours for foundations - Continue installation of underground piping - Continue installation of structural steel - Continue installation of electrical duct banks - Set utility substation
Liquefaction Train 9	- Continued excavation activities - Continued concrete pours for foundations - Commenced installation of underground piping	- Continue excavation activities - Continue concrete pours for foundations - Continue installation of underground piping
EFG	- Continued excavation activities - Commenced concrete pours for foundations - Continued installation of underground piping	- Continue excavation activities - Continue concrete pours for foundations - Continue installation of underground piping
Refrigerant Storage	- Completed piling installations - Commenced excavation activities	- Continue excavation activities - Commence installation of underground piping
Access Roads/Other	Continued construction of heavy haul road	Continue construction of heavy haul road

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
April 2026 Monthly Progress Report

7.0 Permitting and Environmental

Summary of Problems, Non-Compliances, and Corrective Actions

Date	Description
None.	

Agency Contacts/Inspections

Agency	Name	Date	Location/Activity
None.			

8.0 Progress Photos



Photo 1: Train 7 Aboveground Piping Installation



Photo 2: Train 8 Cryogenic Rack Foundation

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
April 2026 Monthly Progress Report



Photo 3: Train 8 Utility Substation Foundation

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
April 2026 Monthly Progress Report



Photo 4: Train 8 Structural Steel

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
April 2026 Monthly Progress Report



Photo 5: End Flash Gas Foundation

**CORPUS CHRISTI LIQUEFACTION STAGE 3 PROJECT
CORPUS CHRISTI LIQUEFACTION MIDSCALE TRAINS 8 & 9 PROJECT**

Corpus Christi, Texas

**MONTHLY PROGRESS REPORT
MAY 2026**

**FERC DOCKET NO. CP18-512-000 (STAGE 3)
FERC DOCKET NO. CP23-129-000 (TRAINS 8 & 9)**

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
May 2026 Monthly Progress Report

Table of Contents

1.0 Executive Summary 3

2.0 Project Highlights 3

3.0 Environmental, Safety, and Health Progress 3

4.0 Schedule 4

5.0 Construction 5

6.0 Permitting and Environmental 8

7.0 Progress Photos..... 9

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
May 2026 Monthly Progress Report

1.0 Executive Summary

On November 22, 2019, the Federal Energy Regulatory Commission (“FERC” or “Commission”) issued an Order Issuing Authority Under Section 3 and Section 7(c) of the Natural Gas Act (“NGA”) (“Order”) granting the necessary authorization to Corpus Christi Liquefaction (“CCL”) for the construction and operation of an expansion of the Corpus Christi Liquefaction Project (“Stage 3 Project”). On March 10, 2025, the FERC issued an Order granting the necessary authorization to CCL for the construction and operation of a second expansion of the Corpus Christi Liquefaction Project (“Midscale Trains 8 & 9 Project”). This report covers activities for the Stage 3 Project and the Midscale Trains 8 & 9 Project during the month of May 2026.

The Stage 3 Project Engineering and Procurement are 99.8% and 100% complete, respectively. Subcontract and direct hire construction work are 97.8% and 95.1% complete, respectively. Overall project completion for the Stage 3 Project is 98.0%.

The Trains 8 & 9 Project Engineering and Procurement are 90.2% and 64.7%, respectively. Subcontract and direct hire construction work are 52.2% and 5.6% complete, respectively. Overall project completion for the Trains 8 & 9 Project is 45.3%.

2.0 Project Highlights

Key work fronts for the Stage 3 Project included aboveground piping in Trains 6 - 7 and outside boundary limits (“OSBL”), concrete pours in Train 7 and OSBL, and structural steel erection in Train 7 and OSBL. Additional continued work includes road improvements, drainage work, and mobilization of temporary facilities, equipment, and personnel.

Key work fronts for the Midscale Trains 8 & 9 Project included excavations, concrete pours, underground piping installation, structural steel installation, and aboveground piping installation.

3.0 Environmental, Safety, and Health Progress

The following table includes health and safety incidents for the Stage 3 Project.

Stage 3 Project								
	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹
Bechtel	19	1,229	23	1,353	1	27	0	2
Subcontractor	0	93	0	22	0	2	0	0
Total	19	1,322	23	1,375	1	29	0	2

1. ITD = Inception to Date.

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
May 2026 Monthly Progress Report

The following table includes health and safety incidents for the Midscale Trains 8 & 9 Project.

Midscale Trains 8 & 9 Project								
	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹
Bechtel	2	9	2	11	0	0	0	0
Subcontractor	0	1	0	3	0	0	0	0
Total	2	10	2	14	0	0	0	0

1. ITD = Inception to Date.

4.0 Schedule

There were no changes to the Stage 3 Project schedule during the reporting period. An additional schedule for the Midscale Trains 8 & 9 Project was provided on April 10, 2025 (Accession No. 202504105188).

5.0 Emergency Response Plan Updates

There were no updates to the Emergency Response Plan for the reporting period. The table below identifies the emergency response committee meetings for 2026.

2026 Committee Meetings		
CCLEPC	STWAC	CPLEPC
January 6, 2026	January 15, 2026	February 19, 2026
March 3, 2026	April 16, 2026	May 21, 2026
May 5, 2026	July 16, 2026	August 20, 2026
July 7, 2026	August 15, 2026	November 19, 2026
September 1, 2026		
November 3, 2026		

Please refer to the following websites for additional information on the emergency response organizations:

- <https://coastalplainlepc.org/>
- <https://www.stwac.org/>
- <https://cclepc.org/wpbuild/>

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
May 2026 Monthly Progress Report

6.0 Construction

The following table includes current and planned construction activities for the Stage 3 Project.

Stage 3 Project		
Area	Construction Activities in Current Month	Planned Work for Next Month
Liquefaction Train 6	- Completed excavation to support the upcoming concrete pours - Completed concrete foundations and pedestal works - Completed installation of structural steel - Continued installation of aboveground piping - Continued insulation of aboveground piping - Continued cable pulls	- Complete installation of aboveground piping - Complete insulation of aboveground piping - Complete cable pulls - Substantial completion
Liquefaction Train 7	- Continued excavation to support the upcoming concrete pours - Continued concrete foundation and pedestal works - Continued installation of structural steel - Continued installation of aboveground piping - Continued insulation of aboveground piping - Continued cable pulls	- Continue excavation to support the upcoming concrete pours - Continue concrete foundation and pedestal works - Continue installation of structural steel - Continue installation of aboveground piping - Continue insulation of aboveground piping - Continue cable pulls
OSBL Area East/West/South	- Continued drainage works at OSBL East and South - Continued installation of reinforced concrete box culverts drains in OSBL East area - Continued excavations in OSBL East and South - Continued concrete foundations and pedestal works in OSBL Phase 2 area - Completed installation of structural steel in OSBL West and South areas - Completed testing of underground piping - Completed installation and testing of aboveground piping - Completed installation of electrical duct banks in OSBL East, West and South areas - Continued cable pulls	- Continue drainage works in OSBL East and South - Continue installation of reinforced concrete box culvert drains in OSBL East area - Continue excavations in OSBL East and South - Continue concrete foundations and pedestal works - Continue cable pulls

Corpus Christi Liquefaction Stage 3 Project
 Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
 May 2026 Monthly Progress Report

Stage 3 Project		
Area	Construction Activities in Current Month	Planned Work for Next Month
Access Roads / Buildings / Other	- Continued road improvements and drainage work <u>O&M Buildings & Welcome Center:</u> - Completed electrical and plumbing work - Completed installation of metal panels and floor - Completed landscaping	Continue road improvements and drainage work

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
May 2026 Monthly Progress Report

The following table includes current and planned construction activities for the Midscale Trains 8 & 9 Project.

Midscale Trains 8 & 9 Project		
Area	Construction Activities in Current Month	Planned Work for Next Month
Liquefaction Train 8	- Continued excavation activities - Continued concrete pours for foundations - Continued installation of underground piping - Continued installation of structural steel - Continued installation of electrical duct banks - Commenced installation of aboveground piping - Set utility substation	- Continue excavation activities - Continue concrete pours for foundations - Continue installation of underground piping - Continue installation of structural steel - Continue installation of electrical duct banks - Continue installation of aboveground piping
Liquefaction Train 9	- Continued excavation activities - Continued concrete pours for foundations - Continued installation of underground piping	- Continue excavation activities - Continue concrete pours for foundations - Continue installation of underground piping - Commence installation of electrical duct banks - Set utility substation
EFG	- Continued excavation activities - Continued concrete pours for foundations - Continued installation of underground piping	- Continue excavation activities - Continue concrete pours for foundations - Continue installation of underground piping
Refrigerant Storage	- Continued excavation activities - Commenced installation of underground piping	- Continue excavation activities - Continue installation of underground piping
Access Roads/Other	- Continued construction of heavy haul road - Completed piling installations in OSBL - Commenced excavation activities in OSBL - Continued excavation activities in Brownfield area - Continued concrete pours in Brownfield area - Continued installation of structural steel in Brownfield area	- Continue construction of heavy haul road - Continue excavation activities in OSBL - Commence concrete pours in OSBL - Continue excavation activities in Brownfield area - Continue concrete pours in Brownfield area - Continue installation of structural steel in Brownfield area - Commence installation of aboveground piping in Brownfield area

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
May 2026 Monthly Progress Report

7.0 Permitting and Environmental

Summary of Problems, Non-Compliances, and Corrective Actions

Date	Description
None.	

Agency Contacts/Inspections

Agency	Name	Date	Location/Activity
None.			

8.0 Progress Photos



Photo 1: Train 7 Cryogenic Rack Area



Photo 2: Train 8 Cryogenic Rack Foundation

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
May 2026 Monthly Progress Report



Photo 3: Train 8 Utility Substation



Photo 4: Train 8 Structural Steel

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
May 2026 Monthly Progress Report



Photo 5: End Flash Gas Foundation

**CORPUS CHRISTI LIQUEFACTION STAGE 3 PROJECT
CORPUS CHRISTI LIQUEFACTION MIDSCALE TRAINS 8 & 9 PROJECT**

Corpus Christi, Texas

**MONTHLY PROGRESS REPORT
JUNE 2026**

**FERC DOCKET NO. CP18-512-000 (STAGE 3)
FERC DOCKET NO. CP23-129-000 (TRAINS 8 & 9)**

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
June 2026 Monthly Progress Report

Table of Contents

1.0	Executive Summary	3
2.0	Project Highlights	3
3.0	Environmental, Safety, and Health Progress	3
4.0	Schedule	4
5.0	Construction	5
6.0	Permitting and Environmental	7
7.0	Progress Photos.....	8

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
June 2026 Monthly Progress Report

1.0 Executive Summary

On November 22, 2019, the Federal Energy Regulatory Commission (“FERC” or “Commission”) issued an Order Issuing Authority Under Section 3 and Section 7(c) of the Natural Gas Act (“NGA”) (“Order”) granting the necessary authorization to Corpus Christi Liquefaction (“CCL”) for the construction and operation of an expansion of the Corpus Christi Liquefaction Project (“Stage 3 Project”). On March 10, 2025, the FERC issued an Order granting the necessary authorization to CCL for the construction and operation of a second expansion of the Corpus Christi Liquefaction Project (“Midscale Trains 8 & 9 Project”). This report covers activities for the Stage 3 Project and the Midscale Trains 8 & 9 Project during the month of June 2026.

The Stage 3 Project Engineering and Procurement are 99.8% and 100% complete, respectively. Subcontract and direct hire construction work are 98.0% and 96.0% complete, respectively. Overall project completion for the Stage 3 Project is 98.4%.

The Trains 8 & 9 Project Engineering and Procurement are 91.5% and 69.9%, respectively. Subcontract and direct hire construction work are 53.4% and 6.7% complete, respectively. Overall project completion for the Trains 8 & 9 Project is 48.3%.

2.0 Project Highlights

Key work fronts for the Stage 3 Project included aboveground piping in Trains 7 and outside boundary limits (“OSBL”), concrete pours in Train 7 and OSBL, and structural steel erection in Train 7. Additional continued work includes road improvements, drainage work, and mobilization of temporary facilities, equipment, and personnel.

Key work fronts for the Midscale Trains 8 & 9 Project included excavations, concrete pours, underground piping installation, structural steel installation, and aboveground piping installation.

3.0 Environmental, Safety, and Health Progress

The following table includes health and safety incidents for the Stage 3 Project.

Stage 3 Project								
	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹
Bechtel	14	1,243	17	1,370	0	27	0	2
Subcontractor	0	93	1	23	0	2	0	0
Total	14	1,336	18	1,393	0	29	0	2

1. ITD = Inception to Date.

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
June 2026 Monthly Progress Report

The following table includes health and safety incidents for the Midscale Trains 8 & 9 Project.

Midscale Trains 8 & 9 Project								
	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹
Bechtel	3	12	1	12	0	0	0	0
Subcontractor	0	1	0	3	0	0	0	0
Total	3	13	1	15	0	0	0	0

1. ITD = Inception to Date.

4.0 Schedule

There were no changes to the Stage 3 Project schedule during the reporting period. An additional schedule for the Midscale Trains 8 & 9 Project was provided on April 10, 2025 (Accession No. 202504105188).

5.0 Emergency Response Plan Updates

There were no updates to the Emergency Response Plan for the reporting period. The table below identifies the emergency response committee meetings for 2026.

2026 Committee Meetings		
CCLEPC	STWAC	CPLEPC
January 6, 2026	January 15, 2026	February 19, 2026
March 3, 2026	April 16, 2026	May 21, 2026
May 5, 2026	July 16, 2026	August 20, 2026
July 7, 2026	August 15, 2026	November 19, 2026
September 1, 2026		
November 3, 2026		

Please refer to the following websites for additional information on the emergency response organizations:

- <https://coastalplainlepc.org/>
- <https://www.stwac.org/>
- <https://cclepc.org/wpbuild/>

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
June 2026 Monthly Progress Report

6.0 Construction

The following table includes current and planned construction activities for the Stage 3 Project.

Stage 3 Project		
Area	Construction Activities in Current Month	Planned Work for Next Month
Liquefaction Train 6	- Completed installation of aboveground piping - Completed insulation of aboveground piping - Completed cable pulls - Substantial completion	
Liquefaction Train 7	- Continued excavation to support the upcoming concrete pours - Continued concrete foundation and pedestal works - Continued installation of structural steel - Continued installation of aboveground piping - Continued insulation of aboveground piping - Continued cable pulls	- Continue excavation to support the upcoming concrete pours - Continue concrete foundation and pedestal works - Complete installation of structural steel - Continue installation of aboveground piping - Continue insulation of aboveground piping - Continue cable pulls
OSBL Area East/West/South	- Continued drainage works at OSBL East and South - Continued installation of reinforced concrete box culverts drains in OSBL East area - Continued excavations in OSBL East and South - Completed concrete foundations and pedestal works in OSBL Phase 2 area - Continued cable pulls	- Continue drainage works in OSBL East and South - Continue installation of reinforced concrete box culvert drains in OSBL East area - Continue excavations in OSBL East and South - Continue cable pulls
Access Roads / Buildings / Other	Continued road improvements and drainage work	Continue road improvements and drainage work

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
June 2026 Monthly Progress Report

The following table includes current and planned construction activities for the Midscale Trains 8 & 9 Project.

Midscale Trains 8 & 9 Project		
Area	Construction Activities in Current Month	Planned Work for Next Month
Liquefaction Train 8	- Continued excavation activities - Continued concrete pours for foundations - Continued installation of underground piping - Continued installation of structural steel - Continued installation of electrical duct banks - Continued installation of aboveground piping	- Continue excavation activities - Continue concrete pours for foundations - Continue installation of underground piping - Continue installation of structural steel - Continue installation of electrical duct banks - Continue installation of aboveground piping - Set liquefaction substation
Liquefaction Train 9	- Continued excavation activities - Continued concrete pours for foundations - Continued installation of underground piping - Commenced installation of electrical duct banks - Set utility substation	- Continue excavation activities - Continue concrete pours for foundations - Continue installation of underground piping - Continue installation of electrical duct banks
EFG	- Continued excavation activities - Continued concrete pours for foundations - Continued installation of underground piping	- Continue excavation activities - Continue concrete pours for foundations - Continue installation of underground piping
Refrigerant Storage	- Continued excavation activities - Continued installation of underground piping	- Continue excavation activities - Continue installation of underground piping
Access Roads/Other	- Continued construction of heavy haul road - Continued excavation activities in OSBL - Continued excavation activities in Brownfield area - Continued concrete pours in Brownfield area - Continued installation of structural steel in Brownfield area - Commenced installation of aboveground piping in Brownfield area	- Continue construction of heavy haul road - Continue excavation activities in OSBL - Continue excavation activities in Brownfield area - Continue concrete pours in Brownfield area - Continue installation of structural steel in Brownfield area - Continue installation of aboveground piping in Brownfield area

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
June 2026 Monthly Progress Report

7.0 Permitting and Environmental

Summary of Problems, Non-Compliances, and Corrective Actions

Date	Description
None.	

Agency Contacts/Inspections

Agency	Name	Date	Location/Activity
PHMSA	Charles Onwuachi, Seth Schreiber, and Thach Nguyen	June 9 – 11, 2026	Stage 3 M6 P&ID Walkdown and Construction Inspection.

The Stage 3 Project Modified Semi-Annual Operations Report for the period of January 1 – June 30, 2026, is provided as **Attachment 1**.

8.0 Progress Photos



Photo 1: Train 7 Cryogenic Rack Area



Photo 2: Train 8 Structural Steel

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
June 2026 Monthly Progress Report



Photo 3: Train 8 Liquefaction Substation Pedestals



Photo 4: Train 9 Utility Substation

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
June 2026 Monthly Progress Report



Photo 5: End Flash Gas Foundation

**CORPUS CHRISTI LIQUEFACTION STAGE 3 PROJECT
CORPUS CHRISTI LIQUEFACTION MIDSCALE TRAINS 8 & 9 PROJECT**

Corpus Christi, Texas

**MONTHLY PROGRESS REPORT
JULY 2026**

**FERC DOCKET NO. CP18-512-000 (STAGE 3)
FERC DOCKET NO. CP23-129-000 (TRAINS 8 & 9)**

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
July 2026 Monthly Progress Report

Table of Contents

1.0	Executive Summary	3
2.0	Project Highlights	3
3.0	Environmental, Safety, and Health Progress	3
4.0	Schedule	4
5.0	Construction	5
6.0	Permitting and Environmental	7
7.0	Progress Photos.....	8

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
July 2026 Monthly Progress Report

1.0 Executive Summary

On November 22, 2019, the Federal Energy Regulatory Commission (“FERC” or “Commission”) issued an Order Issuing Authority Under Section 3 and Section 7(c) of the Natural Gas Act (“NGA”) (“Order”) granting the necessary authorization to Corpus Christi Liquefaction (“CCL”) for the construction and operation of an expansion of the Corpus Christi Liquefaction Project (“Stage 3 Project”). On March 10, 2025, the FERC issued an Order granting the necessary authorization to CCL for the construction and operation of a second expansion of the Corpus Christi Liquefaction Project (“Midscale Trains 8 & 9 Project”). This report covers activities for the Stage 3 Project and the Midscale Trains 8 & 9 Project during the month of June 2026.

The Stage 3 Project Engineering and Procurement are 99.9% and 100% complete, respectively. Subcontract and direct hire construction work are 98.2% and 97.6% complete, respectively. Overall project completion for the Stage 3 Project is 99.0%.

The Trains 8 & 9 Project Engineering and Procurement are 92.7% and 72.7%, respectively. Subcontract and direct hire construction work are 55.4% and 9.8% complete, respectively. Overall project completion for the Trains 8 & 9 Project is 51.0%.

2.0 Project Highlights

Key work fronts for the Stage 3 Project included insulation of aboveground piping in Trains 7. Additional continued work includes road improvements, drainage work, and mobilization of temporary facilities, equipment, and personnel.

Key work fronts for the Midscale Trains 8 & 9 Project included excavations, concrete pours, underground piping installation, structural steel installation, aboveground piping installation, and equipment setting.

3.0 Environmental, Safety, and Health Progress

The following table includes health and safety incidents for the Stage 3 Project.

Stage 3 Project								
	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹
Bechtel	21	1,264	32	1,402	0	27	0	2
Subcontractor	0	93	0	23	0	2	0	0
Total	21	1,357	32	1,425	0	29	0	2

1. ITD = Inception to Date.

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
July 2026 Monthly Progress Report

The following table includes health and safety incidents for the Midscale Trains 8 & 9 Project.

Midscale Trains 8 & 9 Project								
	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹
Bechtel	9	21	11	23	0	0	0	0
Subcontractor	0	1	0	3	0	0	0	0
Total	9	22	11	26	0	0	0	0

1. ITD = Inception to Date.

4.0 Schedule

There were no changes to the Stage 3 Project schedule during the reporting period. An additional schedule for the Midscale Trains 8 & 9 Project was provided on April 10, 2025 (Accession No. 202504105188).

5.0 Emergency Response Plan Updates

There were no updates to the Emergency Response Plan for the reporting period. The table below identifies the emergency response committee meetings for 2026.

2026 Committee Meetings		
CCLEPC	STWAC	CPLEPC
January 6, 2026	January 15, 2026	February 19, 2026
March 3, 2026	April 16, 2026	May 21, 2026
May 5, 2026	July 16, 2026	August 20, 2026
July 7, 2026	August 15, 2026	November 19, 2026
September 1, 2026		
November 3, 2026		

Please refer to the following websites for additional information on the emergency response organizations:

- <https://coastalplainlepc.org/>
- <https://www.stwac.org/>
- <https://cclepc.org/wpbuild/>

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
July 2026 Monthly Progress Report

6.0 Construction

The following table includes current and planned construction activities for the Stage 3 Project.

Stage 3 Project		
Area	Construction Activities in Current Month	Planned Work for Next Month
Liquefaction Train 7	- Completed excavations - Continued concrete foundation and pedestal works - Completed installation of structural steel - Continued installation of aboveground piping - Continued insulation of aboveground piping - Continued cable pulls	- Continue concrete foundation and pedestal works - Continue installation of aboveground piping - Continue insulation of aboveground piping - Continue cable pulls
OSBL Area East/West/South	- Continued drainage works at OSBL East and South - Continued installation of reinforced concrete box culverts drains in OSBL East area - Continued excavations in OSBL East and South - Continued cable pulls	- Continue drainage works in OSBL East and South - Continue installation of reinforced concrete box culvert drains in OSBL East area - Continue excavations in OSBL East and South - Continue cable pulls
Access Roads / Buildings / Other	Continued road improvements and drainage work	Continue road improvements and drainage work

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
July 2026 Monthly Progress Report

The following table includes current and planned construction activities for the Midscale Trains 8 & 9 Project.

Midscale Trains 8 & 9 Project		
Area	Construction Activities in Current Month	Planned Work for Next Month
Liquefaction Train 8	- Continued excavation activities - Continued concrete pours for foundations - Continued installation of underground piping - Continued installation of structural steel - Continued installation of electrical duct banks - Continued installation of aboveground piping	- Continue excavation activities - Continue concrete pours for foundations - Continue installation of underground piping - Continue installation of structural steel - Continue installation of electrical duct banks - Continue installation of aboveground piping - Set liquefaction substation
Liquefaction Train 9	- Continued excavation activities - Continued concrete pours for foundations - Continued installation of underground piping - Continued installation of electrical duct banks	- Continue excavation activities - Continue concrete pours for foundations - Continue installation of underground piping - Continue installation of electrical duct banks
EFG	- Continued excavation activities - Continued concrete pours for foundations - Continued installation of underground piping - Commenced installation of structural steel	- Continue excavation activities - Continue concrete pours for foundations - Continue installation of underground piping - Continue installation of structural steel
Refrigerant Storage	- Continued excavation activities - Commenced concrete pours for foundations - Continued installation of underground piping - Commenced installation of electrical duct banks	- Continue excavation activities - Continue concrete pours for foundations - Continue installation of underground piping - Continue installation of electrical duct banks
Access Roads/Other	- Continued construction of heavy haul road - Continued excavation activities in OSBL - Continued excavation activities in Brownfield area - Continued concrete pours in Brownfield area - Continued installation of structural steel in Brownfield area - Commenced installation of electrical duct banks in OSBL - Continued installation of aboveground piping in Brownfield area	- Continue construction of heavy haul road - Continue excavation activities in OSBL - Continue excavation activities in Brownfield area - Commence concrete pours in OSBL - Continue concrete pours in Brownfield area - Continue installation of structural steel in Brownfield area - Continue installation of electrical duct banks in OSBL - Continue installation of aboveground piping in Brownfield area

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
July 2026 Monthly Progress Report

7.0 Permitting and Environmental

Summary of Problems, Non-Compliances, and Corrective Actions

Date	Description
None.	

Agency Contacts/Inspections

Agency	Name	Date	Location/Activity
None.			

8.0 Progress Photos



Photo 1: OSBL Grading

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
July 2026 Monthly Progress Report



Photo 2: Train 8 Structural Steel



Photo 3: Train 8 Foundations

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
July 2026 Monthly Progress Report



Photo 4: Train 8 Liquefaction Substation Pedestals



Photo 5: End Flash Gas Substation Foundation

**CORPUS CHRISTI LIQUEFACTION STAGE 3 PROJECT
CORPUS CHRISTI LIQUEFACTION MIDSCALE TRAINS 8 & 9 PROJECT**

Corpus Christi, Texas

**MONTHLY PROGRESS REPORT
AUGUST 2026**

**FERC DOCKET NO. CP18-512-000 (STAGE 3)
FERC DOCKET NO. CP23-129-000 (TRAINS 8 & 9)**

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
August 2026 Monthly Progress Report

Table of Contents

1.0	Executive Summary	3
2.0	Project Highlights	3
3.0	Environmental, Safety, and Health Progress	3
4.0	Schedule	4
5.0	Emergency Response Plan Updates	4
6.0	Construction	5
7.0	Permitting and Environmental	7
8.0	Progress Photos.....	8

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
August 2026 Monthly Progress Report

1.0 Executive Summary

On November 22, 2019, the Federal Energy Regulatory Commission (“FERC” or “Commission”) issued an Order Issuing Authority Under Section 3 and Section 7(c) of the Natural Gas Act (“NGA”) (“Order”) granting the necessary authorization to Corpus Christi Liquefaction (“CCL”) for the construction and operation of an expansion of the Corpus Christi Liquefaction Project (“Stage 3 Project”). On March 10, 2025, the FERC issued an Order granting the necessary authorization to CCL for the construction and operation of a second expansion of the Corpus Christi Liquefaction Project (“Midscale Trains 8 & 9 Project”). This report covers activities for the Stage 3 Project and the Midscale Trains 8 & 9 Project during the month of August 2026.

The Stage 3 Project Engineering and Procurement are 99.9% and 100% complete, respectively. Subcontract and direct hire construction work are 98.4% and 98.6% complete, respectively. Overall project completion for the Stage 3 Project is 99.3%.

The Trains 8 & 9 Project Engineering and Procurement are 94.4% and 80.6%, respectively. Subcontract and direct hire construction work are 56.6% and 12.2% complete, respectively. Overall project completion for the Trains 8 & 9 Project is 55.6%.

2.0 Project Highlights

Key work fronts for the Stage 3 Project included insulation of aboveground piping in Trains 7. Additional continued work includes road improvements and drainage work.

Key work fronts for the Midscale Trains 8 & 9 Project included excavations, concrete pours, underground piping installation, structural steel installation, aboveground piping installation, and equipment setting.

3.0 Environmental, Safety, and Health Progress

The following table includes health and safety incidents for the Stage 3 Project.

Stage 3 Project								
	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹
Bechtel	11	1,275	23	1,425	0	27	0	2
Subcontractor	1	94	0	23	0	2	0	0
Total	12	1,369	23	1,448	0	29	0	2

1. ITD = Inception to Date.

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
August 2026 Monthly Progress Report

The following table includes health and safety incidents for the Midscale Trains 8 & 9 Project.

Midscale Trains 8 & 9 Project								
	Near Miss		First Aid		Recordable		Lost Time	
	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹	Month	ITD ¹
Bechtel	10	31	12	35	0	0	0	0
Subcontractor	0	1	0	3	0	0	0	0
Total	10	32	12	38	0	0	0	0

1. ITD = Inception to Date.

4.0 Schedule

There were no changes to the Stage 3 Project schedule during the reporting period. An additional schedule for the Midscale Trains 8 & 9 Project was provided on April 10, 2025 (Accession No. 202504105188).

5.0 Emergency Response Plan Updates

There were no updates to the Emergency Response Plan for the reporting period. The table below identifies the emergency response committee meetings for 2026.

2026 Committee Meetings		
CCLEPC	STWAC	CPLEPC
January 6, 2026	January 15, 2026	February 19, 2026
March 3, 2026	April 16, 2026	May 21, 2026
May 5, 2026	July 16, 2026	August 20, 2026
July 7, 2026	August 15, 2026	November 19, 2026
September 1, 2026		
November 3, 2026		

Please refer to the following websites for additional information on the emergency response organizations:

- <https://coastalplainlepc.org/>
- <https://www.stwac.org/>
- <https://cclepc.org/wpbuild/>

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
August 2026 Monthly Progress Report

6.0 Construction

The following table includes current and planned construction activities for the Stage 3 Project.

Stage 3 Project		
Area	Construction Activities in Current Month	Planned Work for Next Month
Liquefaction Train 7	- Completed concrete foundation and pedestal works - Completed installation of aboveground piping - Continued insulation of aboveground piping - Completed cable pulls - Substantial completion	Complete insulation of aboveground piping
OSBL Area East/West/South	- Continued drainage works at OSBL East and South - Continued installation of reinforced concrete box culverts drains in OSBL East area - Continued excavations in OSBL East and South - Continued cable pulls	- Continue drainage works in OSBL East and South - Continue installation of reinforced concrete box culvert drains in OSBL East area - Continue excavations in OSBL East and South - Continue cable pulls
Access Roads / Buildings / Other	Continued road improvements and drainage work	Continue road improvements and drainage work

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
August 2026 Monthly Progress Report

The following table includes current and planned construction activities for the Midscale Trains 8 & 9 Project.

Midscale Trains 8 & 9 Project		
Area	Construction Activities in Current Month	Planned Work for Next Month
Liquefaction Train 8	- Continued excavation activities - Continued concrete pours for foundations - Continued installation of underground piping - Continued installation of structural steel - Continued installation of electrical duct banks - Continued installation of aboveground piping - Set liquefaction substation	- Continue excavation activities - Continue concrete pours for foundations - Continue installation of underground piping - Continue installation of structural steel - Continue installation of electrical duct banks - Continue installation of aboveground piping
Liquefaction Train 9	- Continued excavation activities - Continued concrete pours for foundations - Continued installation of underground piping - Continued installation of electrical duct banks	- Continue excavation activities - Continue concrete pours for foundations - Continue installation of underground piping - Continue installation of electrical duct banks - Set liquefaction substation
EFG	- Continued excavation activities - Continued concrete pours for foundations - Continued installation of underground piping - Continued installation of structural steel - Commenced installation of electrical duct banks - Commenced installation of aboveground piping	- Continue excavation activities - Continue concrete pours for foundations - Continue installation of underground piping - Continue installation of structural steel - Continue installation of electrical duct banks - Continue installation of aboveground piping
Refrigerant Storage	- Continued excavation activities - Continued concrete pours for foundations - Continued installation of underground piping - Continued installation of electrical duct banks	- Continue excavation activities - Continue concrete pours for foundations - Continue installation of underground piping - Continue installation of electrical duct banks
Access Roads/Other	- Continued construction of heavy haul road - Continued excavation activities in OSBL - Continued excavation activities in Brownfield area - Commenced concrete pours in OSBL - Continued concrete pours in Brownfield area - Continued installation of structural steel in Brownfield area - Continued installation of electrical duct banks in OSBL - Continued installation of aboveground piping in Brownfield area	- Continue construction of heavy haul road - Continue excavation activities in OSBL - Continue excavation activities in Brownfield area - Continue concrete pours in OSBL - Continue concrete pours in Brownfield area - Continue installation of structural steel in Brownfield area - Continue installation of electrical duct banks in OSBL - Continue installation of aboveground piping in Brownfield area

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
August 2026 Monthly Progress Report

7.0 Permitting and Environmental

Summary of Problems, Non-Compliances, and Corrective Actions

Date	Description
None.	

Agency Contacts/Inspections

Agency	Name	Date	Location/Activity
None.			

8.0 Progress Photos

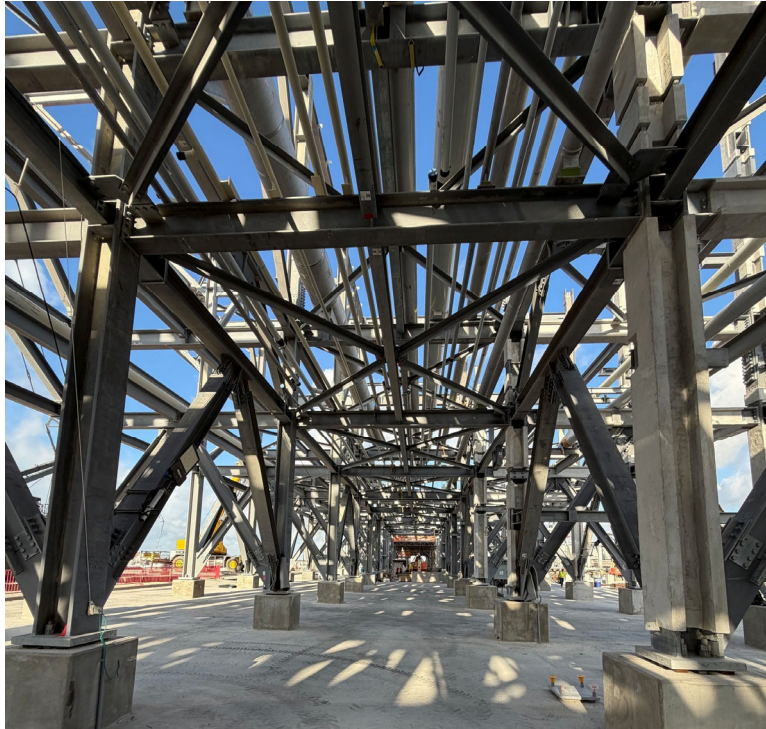


Photo 1: Train 8 Structural Steel and Aboveground Piping



Photo 2: Train 8 Liquefaction Substation

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
August 2026 Monthly Progress Report



Photo 3: End Flash Gas Structural Steel



Photo 4: EFG Substation Foundation

Corpus Christi Liquefaction Stage 3 Project
Corpus Christi Liquefaction Midscale Trains 8 & 9 Project
August 2026 Monthly Progress Report



Photo 5: Refrigerant Storage Foundation
