


Wolf Creek Dam

DSAC I Classification - Karst foundation seepage
\$594M Cost, \$572M Obligated, 93% Complete
Barrier Wall Completed March 2013
Total Project Completion Estimated Summer 2014



Wolf Creek Dam Safety Project Update

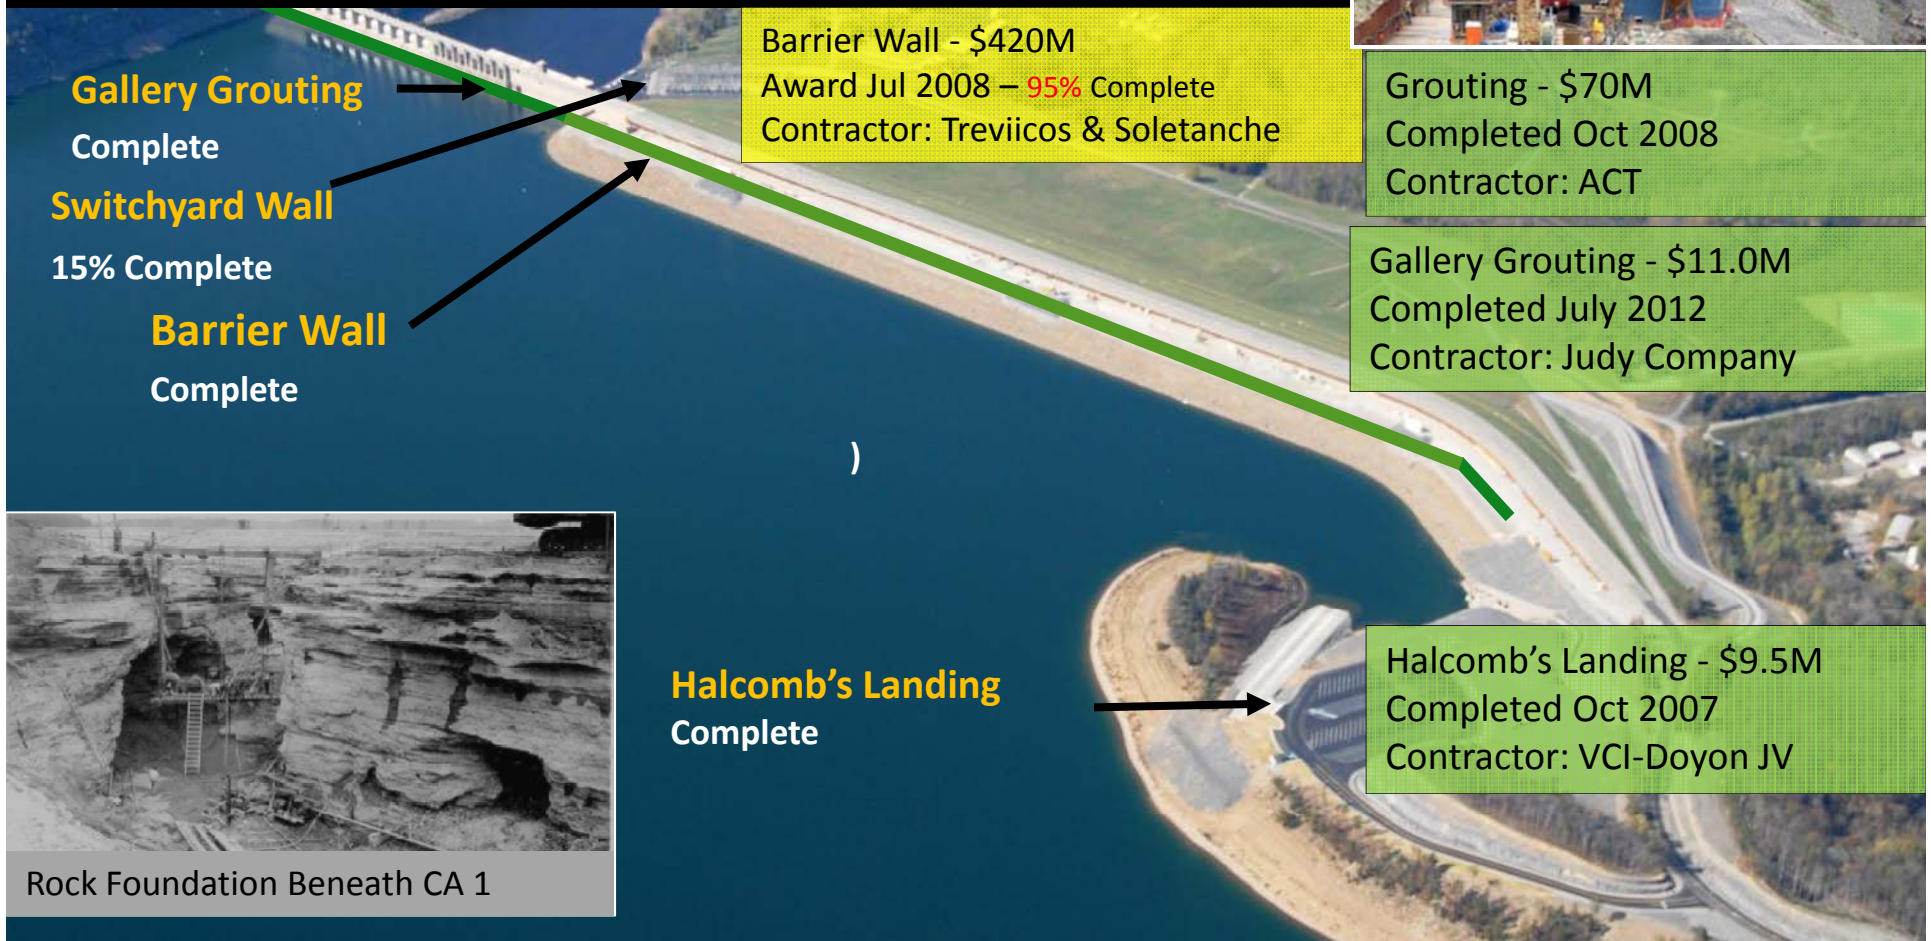

- **Barrier Wall Completed March 2013**
- **Interim Lake Raise April through August 2013 was successful**
- **Downstream switchyard wall and site stabilization construction ongoing now, complete by September 2014**
- **Goal is to return Lake Cumberland to historical operations by Spring 2014**
