

EERE Program Management Guide

A Reference Manual for Program Management

December 2007

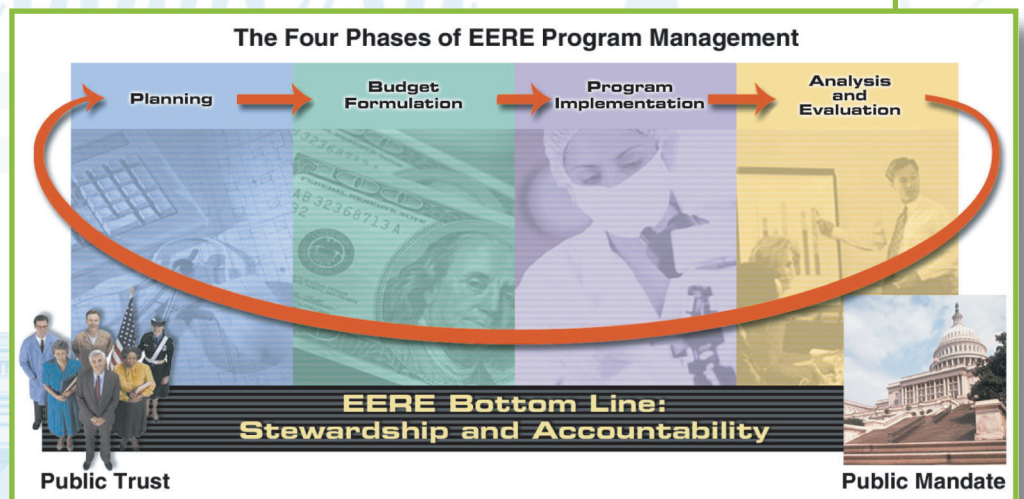


Table of Contents

Introduction

Introduction.....	i-1
-------------------	-----

Chapter 1 Background

1.1 About the U.S. Department of Energy.....	1-1
1.2 About the Office of Energy Efficiency and Renewable Energy.....	1-10

Chapter 2 EERE Business Model and Management System

2.1 EERE Programs as Key Mission Elements.....	2-1
2.2 Distinctions Among EERE Programs, Projects, and Agreements.....	2-3
2.3 EERE Programs and Subprograms.....	2-5
2.4 Roles and Responsibilities of Headquarters and Field Activities.....	2-17
2.5 Program Management Vis-à-vis Project Management Responsibilities.....	2-18
2.6 How to Manage an EERE Program: A Macro Look at the Program Management Team’s Job and the Program Management Cycle.....	2-21
2.7 EERE Strategic Management System.....	2-31

Chapter 3 EERE Communications and Outreach

3.1 EERE Communications and Outreach Overview.....	3-1
3.2 EERE Board of Directors.....	3-10
3.3 Technology Development Communications and Outreach.....	3-16
3.4 Project Management Center Communications and Outreach.....	3-19

Chapter 4 EERE Planning

4.1 Planning Overview.....	4-1
4.2 EERE Strategic Planning.....	4-9
4.3 EERE Multi-Year Program Planning and Crosscutting Planning.....	4-17
4.4 Annual Operations Planning.....	4-23
4.5 Planning Process Summary.....	4-25
4.6 EERE SMS Planning Stages.....	4-27

Chapter 5 EERE Budget Formulation

5.1 Budget Formulation Overview.....	5-1
5.2 Field Budget Call.....	5-10
5.3 EERE Spring Budget Review.....	5-11
5.4 DOE Corporate Program Review Budget.....	5-16
5.5 OMB Request.....	5-22
5.6 Congressional Budget Process.....	5-26
5.7 Performance Budget Formulation Stage.....	5-35

Chapter 6 EERE Program Implementation

6.1 Program Implementation Overview.....	6-1
6.2 Program Implementation Funding Orders	6-3
6.3 Execution Planning.....	6-8
6.4 The Funding Process.....	6-11
6.5 Procurement Planning.....	6-15
6.6 The Multi-Year Procurement (Acquisition and Financial Assistance) Process.....	6-18
6.7 Other Procurement Considerations	6-30
6.8 EERE SMS Program Implementation Stage.....	6-33

Chapter 7 EERE Analysis and Evaluation

7.1 Analysis and Evaluation Overview.....	7-1
7.2 Mission and Roles.....	7-3
7.3 Program Analysis.....	7-5
7.4 Program Evaluation	7-8
7.5 EERE SMS Analysis and Evaluation Stage.....	7-12

Chapter 8 EERE Information and Business Management Systems

8.1 Introduction.....	8-1
8.2 DOE and Field Systems and Interfaces Applicable to EERE.....	8-3
8.3 EERE Corporate Planning System.....	8-5
8.4 EERE Information System.....	8-11
8.5 Windows-Based Systems Approach to Grants Administration	8-17
8.6 Other EERE Information and Business Management Tools	8-19
8.7 Electronic Government	8-23

Appendices

A	Summary of EERE Multi-Year Program Plan Template	A-1
B	Suggested Practice—Developing the Annual Operating Plan, Phase II Guidance	B-1
C	Suggested Practice—Program Progress, Review Process, Phase II Guidance	C-1
D	EERE Peer Review Guide	D-1
E	Suggested Framework for Merit Review	E-1
F	Model Position Description for Deputy Assistant Secretary for the Office of Technology Development	F-1
G	Model Position Description for EERE Program Managers	G-1
H	Model Senior Executive Services Performance Appraisal	H-1
I	EERE Program Management Virtual University	I-1
J	Inherently Governmental Functions	J-1
K	Roles, Responsibilities and Relationships of Program Managers, Project Managers, Contracting Officers and Contracting Officer’s Representatives	K-1
L	Role of the National Laboratories	L-1
M	Support Services	M-1
N	EERE Guidelines, Definitions and Restrictions for Support Services Contracting	N-1
O	List of Acronyms	O-1
P	Reference Guide	P-1
Q	Glossary of Terms	Q-1
